

Memorandum



Date: April 14, 2011

RTC
Agenda Item No. 7(C)

To: Honorable Chairman Bruno A. Barreiro
and Members, Regional Transportation Committee

From: Alina T. Hudak
County Manager

A handwritten signature in black ink, appearing to read "Alina T. Hudak". The signature is written over the printed name in the "From:" field.

Subject: Monthly Report from the Florida Department of Transportation on the Miami Intermodal Center


Attached is a report provided by the Florida Department of Transportation regarding the Miami Intermodal Center Program. The report responds to a request that a program status be provided on a monthly basis.

A large, stylized handwritten signature in black ink, appearing to read "Alina T. Hudak". The signature is written over a horizontal line.

Assistant County Manager



Miami Intermodal Center



March 23, 2011

Honorable Commissioner Bruno Barreiro
District 5
Stephen P. Clark Center
111 N.W. 1st Street, Suite 220
Miami, Florida 33128

Subject: Miami Intermodal Center (MIC) Monthly Progress Report to the Miami-Dade Board of County Commissioners Regional Transportation Committee

Dear Commissioner Barreiro:

I have enclosed, for your information and use, the MIC Program Progress report for the period ending February 28, 2011.


As always, I look forward to working with you and the committee on this most important program. If you have any additional questions, please feel free to contact me at 305-470-5145.

Sincerely,


Gary L. Donn, P.E.
Director and MIC Project Manager

Enclosure

C: Gus Pego, P.E., District Secretary
Ysela Llord, Miami-Dade County
Ric Katz, Kommunikatz, Inc.




Miami Intermodal Center



MIAMI INTERMODAL CENTER (MIC) PROGRAM PROGRESS REPORT TO THE MIAMI-DADE COUNTY BOARD OF COUNTY COMMISSIONERS REGIONAL TRANSPORTATION COMMITTEE

February 2011
(Volume 4, #3)

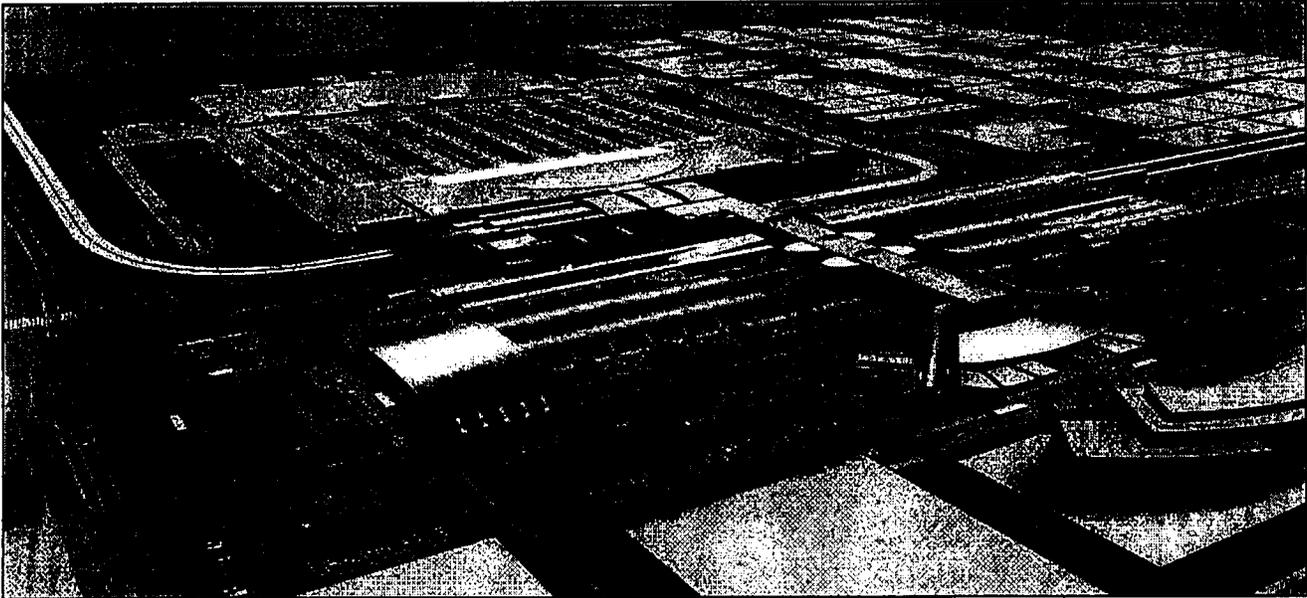

MIC Central Station

The following is the Monthly Status Report for work placed through February 28, 2011:

Rental Car Center (RCC)

- The Rental Car Center began Operations – July 13, 2010
- All major elements of construction **have been completed**; The CO was issued March 8, 2011.
- Miscellaneous Operational issues have been identified and are being addressed by the Department and MDAD.

Rental Car Center (RCC) – Industry Meeting

- Beginning October 7, 2010 Bi-monthly meetings commenced with the Rental Car Companies; the next scheduled meeting is April 7, 2011. With this meeting, the bi-monthly industry meetings will transition from a construction meeting, conducted by FDOT, to operational meetings that will be conducted by MDAD staff.

Roadways

- The Roadway Improvement Program has been completed.

MIA Mover (APM) and MIC/MIA Station

- Monthly coordination meetings between owners and contractors/designer are on-going.
- All construction of the MIC/MIA Station has been completed by Turner Construction; final completion is scheduled for January 21, 2011.

Central Station Transit Hub

- The Department has provided 100% construction plans to Turner Construction for pricing and finalization of GMP#6C; GMP#6c negotiations are expected to be completed by March 31, 2011. Permits from the Miami-Dade County Building Department are currently under review. The NTP is currently scheduled for April 15, 2011, with construction scheduled to be completed May 2013.

Landscaping

- Construction of the Landscaping on the LeJeune Road Corridor and the RCC has been completed.

SFRTA (Tri-Rail)

- Due to the pending construction of the MIC Central Station, the SFRTA Board approved a relocation agreement with the Department, January 28, 2011, to cease operations at the Miami Airport Station, and resume those operations at the Hialeah Market Station; The Hialeah Market Place station will become the southern terminus of the SFRTA commuter rail system line, until the completion of the MIC Central Station in May 2013. The department is planning to begin the demolition and remediation of the Miami Airport Station as soon as a number of issues with CSXT have been settled.

Construction Schedule

- The current Summary Program Schedule is attached for your information and use. Below is the current construction milestones contained in that schedule.

Construction Projects	Start	Finish	Status
MIC/MIA Interchange & LeJeune Road	DECE07	MAY08	COMPLETED
Temporary Tri-Rail Station			CANCELLED
NW 11th Ave & 20th Street	APR08	MAY08	COMPLETED
Rental Car Center	FEB07	JULY10	COMPLETED
MIA Mover Full Station (MDAD)	JAN09	SEPT11	UNDER CONSTRUCTION
MIA Mover Airport Station (MDAD)	JAN09	SEPT11	UNDER CONSTRUCTION
Metrorail Extension to MIC (MDT)	JAN09	APR12	UNDER CONSTRUCTION
MIC Central Station	APR11	MAY13	UNDER NEGOTIATIONS

Budget - Approved Program Budget is \$1.7 billion.
