

# Memorandum



**Date:** July 11, 2011

**To:** Honorable Chairman Bruno A. Barreiro  
and Members, Regional Transportation Committee

**From:** Alina T. Hudak  
County Manager

**Subject:** Monthly Report from the Florida Department of Transportation on the Miami Intermodal Center

RTC  
Agenda Item No. 7(B)

A handwritten signature in black ink, appearing to read "Alina T. Hudak".

---

Attached is a report provided by the Florida Department of Transportation regarding the Miami Intermodal Center Program. The report responds to a request that a program status be provided on a monthly basis.

A handwritten signature in black ink, appearing to read "Alina T. Hudak".  
Assistant County Manager

**FIELD OFFICE**

1845 NW 25th Street  
Miami, Florida 33142

www.micdot.com  
1 358 838 5355

## Miami Intermodal Center



June 20, 2011

Honorable Commissioner Bruno Barreiro  
District 5  
Stephen P. Clark Center  
111 NW 1<sup>st</sup> Street, Suite 220  
Miami, Florida 33128

**Subject: Miami Intermodal Center (MIC) Monthly Progress Report to the Miami-Dade Board of County Commissioners Regional Transportation Committee**

Dear Commissioner Barreiro:

I have enclosed, for your information and use, the MIC Program Progress report for the period ending May 31, 2011.

As always, I look forward to working with you and the committee on this most important program. If you have any additional questions, please feel free to contact me at 305-470-5197.

Sincerely,

Gus Pego  
District Secretary

Enclosure

C: L. Carl Filer, P.E, FDOT  
Ysela Llort, Miami-Dade County  
Ric Katz, Kommunikatz, Inc.

**FIELD OFFICE**

1245 NW 25th Street  
Miami, Florida 33147


www.micccf.com  
1 888 838 5385

# Miami Intermodal Center



## MIAMI INTERMODAL CENTER (MIC) PROGRAM PROGRESS REPORT TO THE MIAMI-DADE COUNTY BOARD OF COUNTY COMMISSIONERS REGIONAL TRANSPORTATION COMMITTEE

May 2011  
(Volume 4, #7)

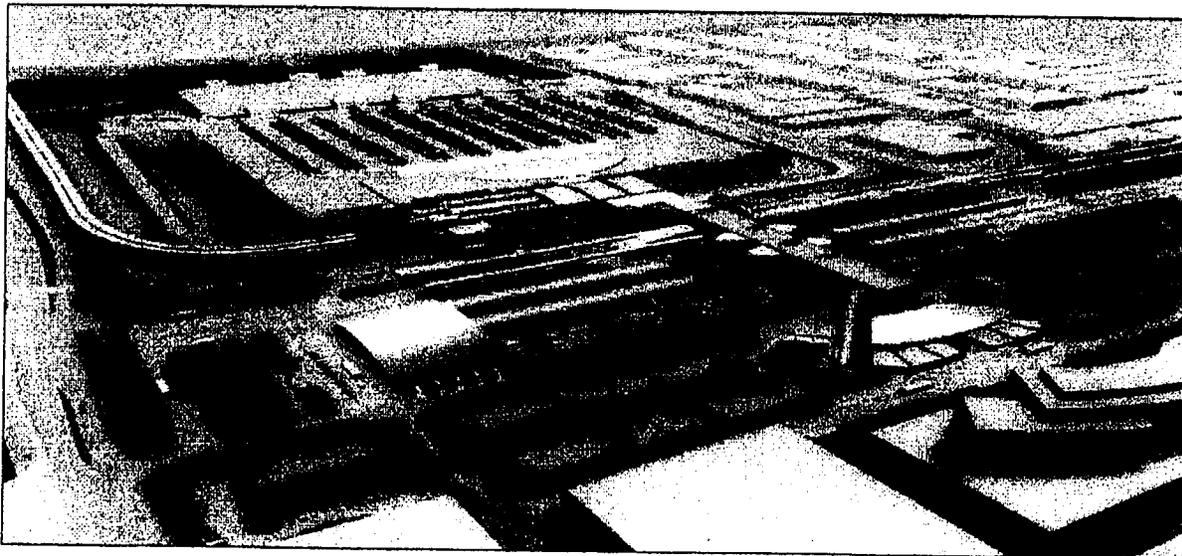

**MIC Central Station**

The following is the Monthly Status Report for work placed through May 31, 2011:

### **Rental Car Center (RCC)**

- The Rental Car Center began Operations – July 13, 2010
- All major elements of construction **have been completed**; The CO was issued March 8, 2011.
- Miscellaneous Operational issues have been identified and are being addressed by the Department and MDAD.

### **Rental Car Center (RCC) – Industry Meeting**

- Beginning October 7, 2010 Bi-monthly meetings commenced with the Rental Car Companies; the next scheduled meeting is July 7, 2011. The bi-monthly industry meetings have transitioned from a construction meeting, conducted by FDOT, to operational meetings conducted by MDAD staff.

**Roadways**

- The Roadway Improvement Program has been completed.

**MIA Mover (APM) and MIC/MIA Station**

- All construction of the MIC/MIA Station has been completed by Turner Construction. The CO was issued on January 20, 2011 and Final completion was achieved on January 24, 2011.

**Central Station Transit Hub**

- The Department has provided 100% construction plans to Turner Construction for pricing and finalization of GMP#6C; GMP#6C negotiations were completed on May 16, 2011. Turner is in the process of obtaining permits from the Miami-Dade County Building Department. Turner Construction received the NTP on May 18, 2011, and construction officially began June 3, 2011. Construction is scheduled to be completed by September 2013.

**Landscaping**

- Construction of the Landscaping on the LeJeune Road Corridor and the RCC has been completed.

**SFRTA (Tri-Rail)**

- Due to the pending construction of the MIC Central Station, the SFRTA Board approved a relocation agreement with the Department on January 28, 2011, to cease operations at the Miami Airport Station, and resume those operations at the Hialeah Market Station. The Hialeah Market Place station will become the southern terminus of the SFRTA commuter rail system line, until the completion of the MIC Central Station in September 2013. The department is planning to begin the demolition and remediation of the Miami Airport Station as soon as a number of issues with CSXT have been settled.

**Construction Schedule**

- The current Summary Program Schedule is attached for your information and use. Below is the current construction milestones contained in that schedule.

Construction Projects	Start	Finish	Status
MIA Mover System (MDAD)	FEB05	MAY08	COMPLETED
Temporary Tri-Rail Station			CANCELLED
North Dade Street	APR08	MAY09	COMPLETED
Rental Car Center	FEB07	JULY10	COMPLETED
MIA Mover Station (MDAD)	FEB08	JAN11	COMPLETED
MIA Mover System (MDAD)	JAN09	DEC11	UNDER CONSTRUCTION
MIA Mover Station (MDAD)	JAN09	SEP11	UNDER CONSTRUCTION
Metrorail Extension to MIC (MDT)	JAN09	APR12	UNDER CONSTRUCTION
MIC Central Station	MAY11	SEP13	NTP ISSUED

**Budget** - Approved Program Budget is \$1.7 billion.

