

Memorandum



Date: March 12, 2012

To: Honorable Chairman Bruno A. Barreiro
and Members, Regional Transportation Committee

From: Carlos A. Gimenez
Mayor 

Subject: Monthly Report from the Florida Department of Transportation on the Miami Intermodal Center

RTC
Agenda Item No. 6(A)

Attached is a report provided by the Florida Department of Transportation regarding the Miami Intermodal Center Program. The report responds to a request that a program status be provided on a monthly basis.



Deputy Mayor



Florida Department of Transportation

RICK SCOTT
GOVERNOR

1000 NW 111 Avenue
Miami, Florida 33172-5800

ANANTH PRASAD, P.E.
SECRETARY

February 16, 2012

Honorable Commissioner Bruno Barreiro
District 5
Stephen P. Clark Center
111 NW 1st Street, Suite 220
Miami, Florida 33128

Subject: Miami Intermodal Center (MIC) Monthly Progress Report to the Miami-Dade Board of County Commissioners Regional Transportation Committee

Dear Commissioner Barreiro:

I have enclosed, for your information and use, the MIC Program Progress report for the period ending January 31, 2012.

As always, I look forward to working with you and the committee on this most important program. If you have any additional questions, please feel free to contact me at 305-470-5197.

Sincerely,

Gus Pego, P.E.
District Secretary

Enclosure

C: L. Carl Filer, P.E, FDOT
Ysela Llort, MDT
Ric Katz, Kommunikatz, Inc.

FIELD OFFICE

1715 NW 20th Street
Miami, Florida 33142


www.micdot.com
1-866-835-5355

Miami Intermodal Center



MIAMI INTERMODAL CENTER (MIC) PROGRAM PROGRESS REPORT TO THE MIAMI-DADE COUNTY BOARD OF COUNTY COMMISSIONERS REGIONAL TRANSPORTATION COMMITTEE

January, 2012
(Volume 5, #2)

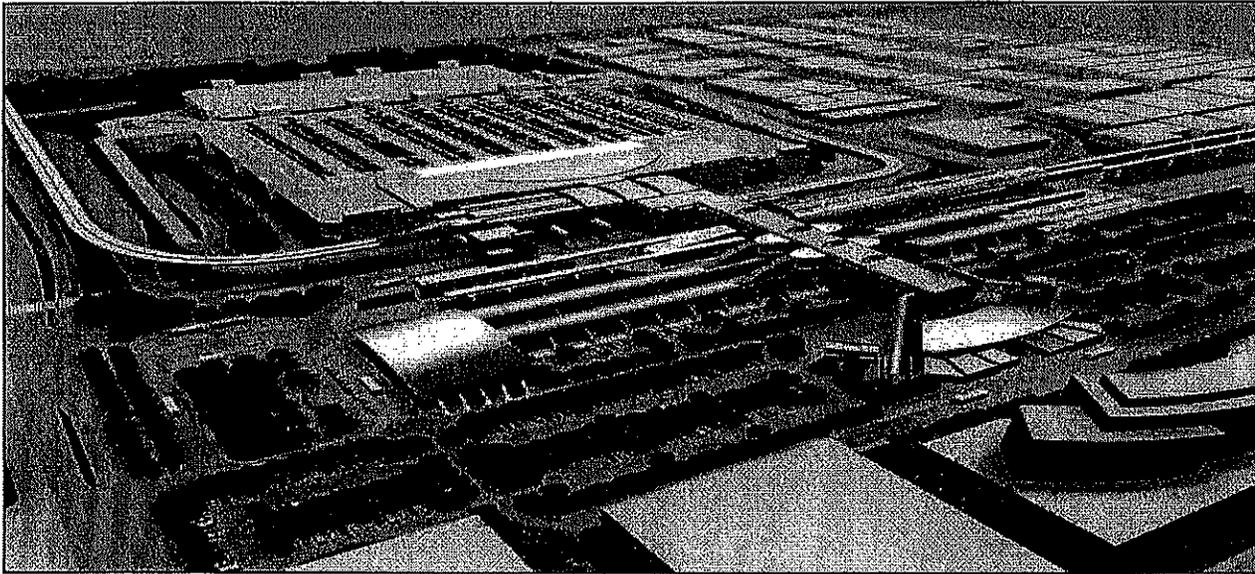

MIC Central Station

The following is the Monthly Status Report for work placed through January 31, 2012:

Rental Car Center (RCC)

- The Rental Car Center began Operations – July 13, 2010
- All major elements of construction have been completed; The CO was issued March 8, 2011 and Final completion was achieved on May 16, 2011.
- The Rental Car Center was conveyed to Miami-Dade County per Quitclaim Deed dated December 20, 2011.

Rental Car Center (RCC) – Industry Meeting

- Beginning October 7, 2010 Bi-monthly meetings commenced with the Rental Car Companies; the next scheduled meeting is February 2, 2012. The bi-monthly industry meetings have transitioned from a construction meeting, conducted by FDOT, to operational meetings conducted by MDAD staff.

Roadways

- The Roadway Improvement Program has been completed.

MIA Mover (APM) and MIC/MIA Station

- All construction of the MIC/MIA Station has been completed by Turner Construction. The CO was issued on January 20, 2011, and Final completion was achieved on January 24, 2011.

Central Station Transit Hub

- The Department has provided 100% construction plans to Turner Construction for pricing and finalization of GMP#6C; GMP#6C negotiations were completed on May 16, 2011. Turner is in the process of obtaining permits from the Miami-Dade County Building Department. Turner Construction received the NTP on May 18, 2011, and construction officially began June 3, 2011. Construction is scheduled to be completed by October 2013.

Landscaping

- Construction of the Landscaping on the LeJeune Road Corridor and the RCC has been completed.

SFRTA (Tri-Rail)

- Due to the pending construction of the MIC Central Station, the SFRTA Board approved a relocation agreement with the Department on January 28, 2011, to cease operations at the Miami Airport Station, and resume those operations at the Hialeah Market Station. The Hialeah Market Place station will become the southern terminus of the SFRTA commuter rail system line, until the completion of the MIC Central Station in October 2013. Tri-Rail has ceased operations at Miami Airport Station as of September 12, 2011.

Construction Schedule

- The current Summary Program Schedule is attached for your information and use. Below is the current construction milestones contained in that schedule.

| Construction Projects | Start | Finish | Status |
|---|--------------|----------------|---------------------------|
| MIC/MIA Interchange & LeJeune Road | FEB09 | MAY08 | COMPLETED |
| Temporary Tri-Rail Station | | | CANCELLED |
| NW 23rd & 29th Streets | APR08 | MAY09 | COMPLETED |
| Rental Car Center | FEB07 | JULY10 | COMPLETED |
| MIA Mover MIC Station (FDOD) | FEB08 | JAN11 | COMPLETED |
| MIA Mover System (MDAD) | JAN09 | SEPT 11 | COMPLETED |
| MIA Mover MIA Station (MDAD) | JAN09 | SEPT11 | COMPLETED |
| Metrorail Extension to MIC (MDT) | JAN09 | APR12 | UNDER CONSTRUCTION |
| MIC Central Station | MAY11 | OCT13 | UNDER CONSTRUCTION |

Budget - Approved Program Budget is \$2.0 billion.

