

Memorandum



Date: October 9, 2013

To: Honorable Chairman Dennis C. Moss
and Members, Transportation and Aviation Committee

From: Carlos A. Gimenez
Mayor

A handwritten signature in black ink, appearing to read "Carlos A. Gimenez".

Subject: Monthly Report from the Florida Department of Transportation on the Miami Intermodal Center

TAC
Agenda Item No. 7C

Attached is a report provided by the Florida Department of Transportation regarding the Miami Intermodal Center Program. The report responds to a request for a monthly program status.

A handwritten signature in black ink, appearing to read "Jack Osterholt".

Jack Osterholt, Deputy Mayor



Florida Department of Transportation

RICK SCOTT
GOVERNOR

1000 NW 111 Avenue
Miami, Florida 33172-5800

ANANTH PRASAD, P.E.
SECRETARY

August 8, 2013

The Honorable Dennis Moss
Chairman, Transportation and Aviation Committee
Miami-Dade Board of County Commissioners, District 9
Stephen P. Clark Center
111 NW 1st Street, Suite 320
Miami, Florida 33128

Subject: Miami Intermodal Center (MIC) Monthly Progress Report to the Miami-Dade Board of County Commissioners Transportation and Aviation Committee

Dear Chairman Moss:

I have enclosed, for your information and use, the MIC Program Progress report for the period ending July 31, 2013.

As always, I look forward to working with you and the committee on this most important program. If you have any additional questions, please feel free to contact me at 305-470-5197.

Sincerely,


Gus Pego, P.E.
District Secretary

Enclosure

cc: L. Carl Filer, P.E, FDOT
Ysela Lfort, MDT
Ric Katz, Kommunikatz, Inc.

MIAMI INTERMODAL CENTER (MIC) PROGRAM PROGRESS REPORT TO THE MIAMI-DADE COUNTY BOARD OF COUNTY COMMISSIONERS TRANSPORTATION AND AVIATION COMMITTEE

July, 2013
(Volume 6, #8)

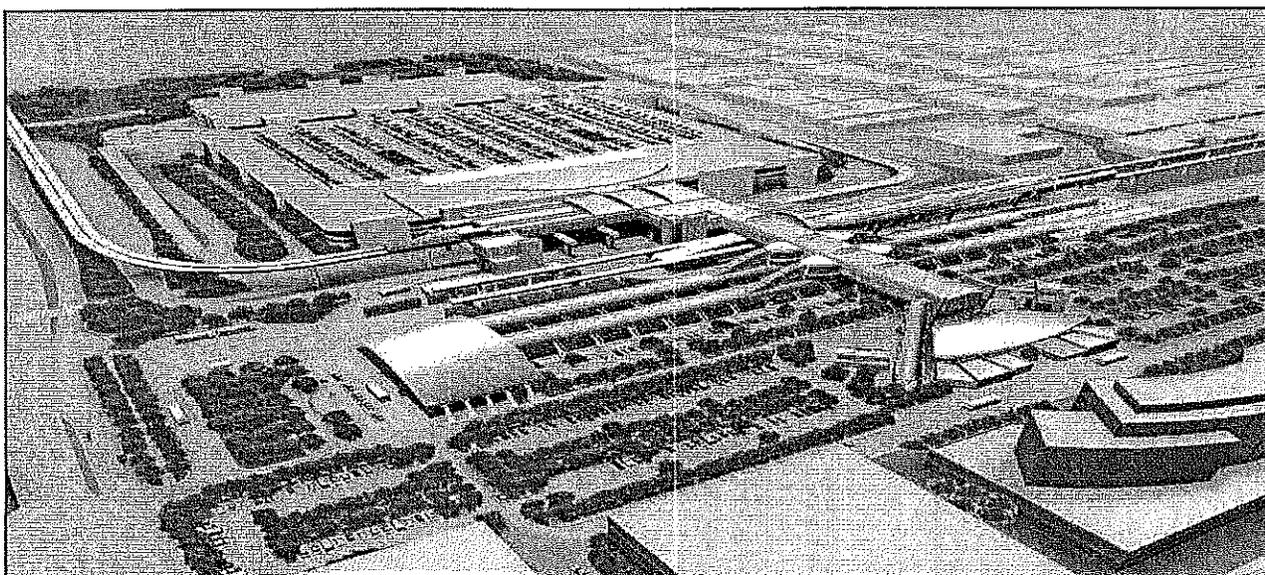

MIC Central Station

The following is the Monthly Status Report for work placed through July 31, 2013:

Rental Car Center (RCC)

- The Rental Car Center began Operations – July 13, 2010
- All major elements of construction **have been completed**; The CO was issued March 8, 2011 and Final completion was achieved on May 16, 2011.
- The Rental Car Center was conveyed to Miami-Dade County per Quitclaim Deed dated December 20, 2011.

Rental Car Center (RCC) – Industry Meeting

- Beginning October 7, 2010 Bi-monthly meetings commenced with the Rental Car Companies; the next scheduled meeting is November 7, 2013. The bi-monthly industry meetings have transitioned from a construction meeting, conducted by FDOT, to operational meetings conducted by MDAD staff.

Roadways

- The Roadway Improvement Program has been completed.

MIA Mover (APM) and MIC/MIA Station

- All construction of the MIC/MIA Station has been completed by Turner Construction. The CO was issued on January 20, 2011, and Final completion was achieved on January 24, 2011.

Central Station Transit Hub

- The Department has provided 100% construction plans to Turner Construction for pricing and finalization of GMP#6C; GMP#6C negotiations were completed on May 16, 2011. Turner Construction received the NTP on May 18, 2011, and construction officially began June 3, 2011. Construction is scheduled to be completed early 2014. Turner to continue coordinating building construction, mechanical room, canopies over the head houses. GTC and railroad platforms, MEP installations, escalator and elevator installations, parking lot and roadway construction and railroad platform construction. Options for Amtrak platform extension are being analyzed including southern track extension and NW 28th. Street runaround road. NW 25th. Street will reopen October 2013.

Landscaping

- Construction of the Landscaping on the LeJeune Road Corridor and the RCC has been completed.

SFRTA (Tri-Rail)

- Due to the pending construction of the MIC Central Station, the SFRTA Board approved a relocation agreement with the Department on January 28, 2011, to cease operations at the Miami Airport Station, and resume those operations at the Hialeah Market Station. The Hialeah Market Place station will become the southern terminus of the SFRTA commuter rail system line, until the completion of the MIC Central Station in late 2013. Tri-Rail has ceased operations at Miami Airport Station as of September 12, 2011.

Construction Schedule

- The current Summary Program Schedule is attached for your information and use. Below is the current construction milestones contained in that schedule.

Construction Projects	Start	Finish	Status
MIC/MIA Interchange & LeJeune Road	FEB05	MAY08	COMPLETED
Temporary Tri-Rail Station			CANCELLED
NW 21 st , 28 th & 29 th Streets	APR08	MAY09	COMPLETED
Rental Car Center	FEB07	JULY10	COMPLETED
MIA Mover MIC Station (FDOT)	FEB08	JAN11	COMPLETED
MIA Mover System (MDAD)	JAN09	SEPT 11	COMPLETED
MIA Mover MIA Station (MDAD)	JAN09	SEPT 11	COMPLETED
Metrorail Extension to MIC (MDT)	JAN09	JUL 12	COMPLETED
MIC Central Station	MAY11	EARLY 14	UNDER CONSTRUCTION

Budget - Approved Program Budget is \$2.0 billion.

