


**Start Date** 31JUL00  
**Finish Date** 05FEB04  
**Data Date** 30AUG00  
**Run Date** 27SEP00 10:31

**MIAMI-DADE PARK & RECREATION DEPARTMENT**

**Sheet 1 of 3**

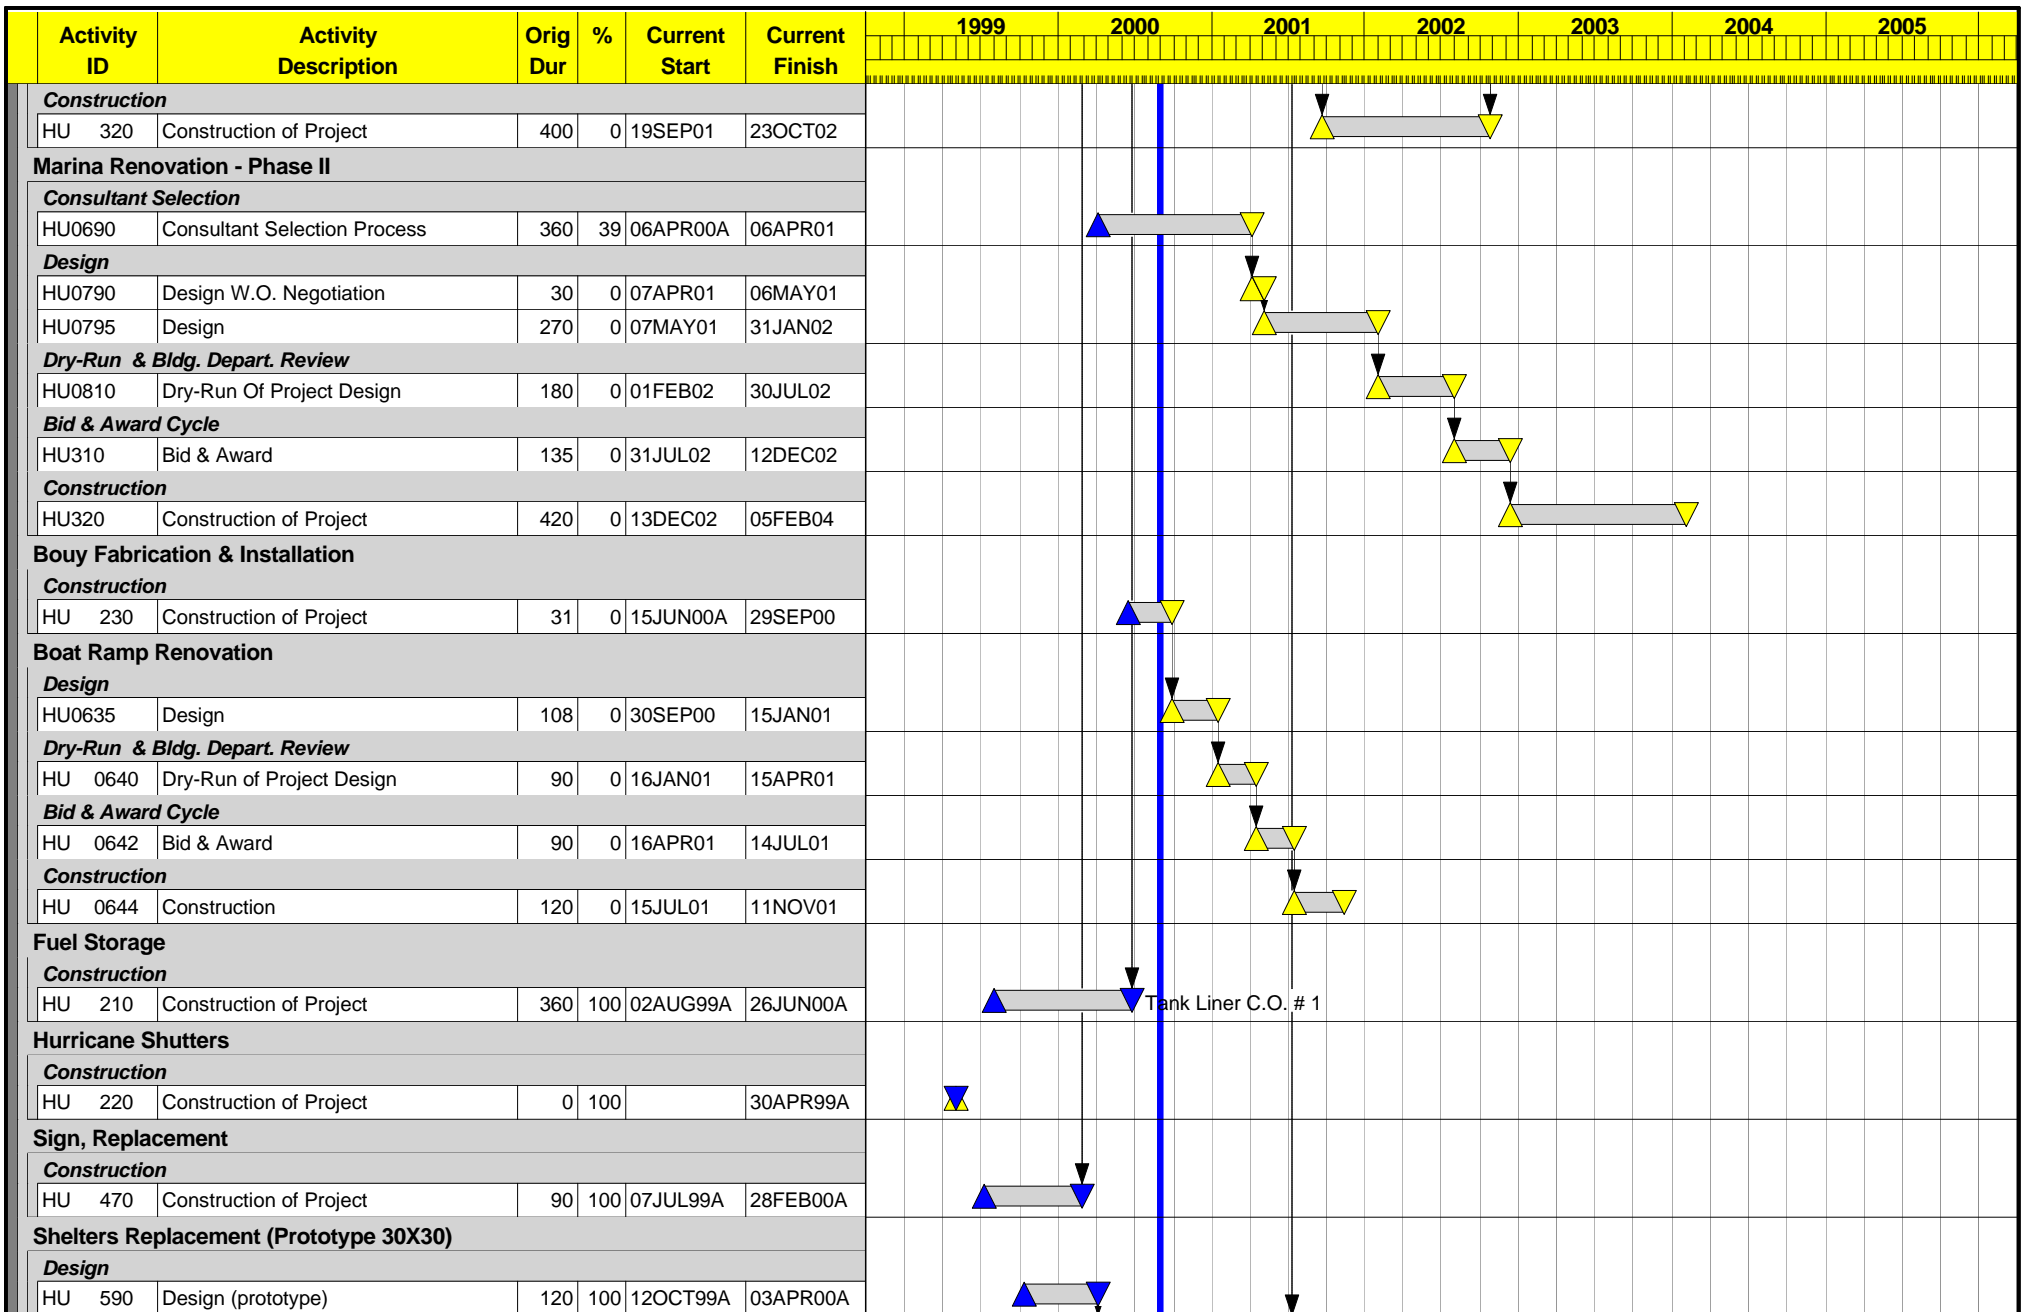

**Start Date** 31JUL00  
**Finish Date** 05FEB04  
**Data Date** 30AUG00  
**Run Date** 27SEP00 10:31

**MIAMI-DADE PARK & RECREATION DEPARTMENT**

**Sheet 2 of 3**

Activity ID	Activity Description	Orig Dur	%	Current Start	Current Finish	1999												2000												2001												2002												2003												2004												2005											
<b>Design</b>																																																																																									
HU 592	Site Design	1	0	04APR00A	04NOV00																																																																																				
<b>Dry-Run &amp; Bldg. Depart. Review</b>																																																																																									
HU 600	Dry-Run of Project Design (site)	37	0	05NOV00	11DEC00																																																																																				
<b>Bid &amp; Award Cycle</b>																																																																																									
HU 610	Bid & Award	90	0	12DEC00	11MAR01																																																																																				
<b>Construction</b>																																																																																									
HU 620	Construction of Project	120	0	12MAR01	09JUL01																																																																																				
<b>Sewer Connection</b>																																																																																									
<b>Planning</b>																																																																																									
HU 8000	See DERM Sewer Consent Agreem.	1	0	30AUG00	30AUG00																																																																																				
<b>Wood Fence Boat Ramp</b>																																																																																									
<b>Construction</b>																																																																																									
HU 630	Construction of Project	0	100		06AUG99A																																																																																				

**Start Date** 31JUL00  
**Finish Date** 05FEB04  
**Data Date** 30AUG00  
**Run Date** 27SEP00 10:31

© Primavera Systems, Inc.

MIAMI-DADE PARK & RECREATION DEPARTMENT

Sheet 3 of 3
