

# Memorandum



**Date:** March 13, 2013

**To:** Honorable Chairman Dennis C. Moss  
and Members, Transportation and Aviation Committee

**From:** Carlos A. Gimenez  
Mayor

**Subject:** Monthly Report from the Florida Department of Transportation on the Miami Intermodal Center

TAC

Agenda Item No. 7A

---

Attached is a report provided by the Florida Department of Transportation regarding the Miami Intermodal Center Program. The report responds to a request for a monthly program status.

A handwritten signature in cursive script, likely belonging to Jack Osterholt.

Jack Osterholt, Deputy Mayor



*Florida Department of Transportation*

RICK SCOTT  
GOVERNOR

1000 NW 111 Avenue  
Miami, Florida 33172-5800

ANANTH PRASAD, P.E.  
SECRETARY

February 15, 2013

The Honorable Dennis Moss  
Chairman, Transportation and Aviation Committee  
Miami-Dade Board of County Commissioners, District 9  
Stephen P. Clark Center  
111 NW 1st Street, Suite 320  
Miami, Florida 33128

**Subject: Miami Intermodal Center (MIC) Monthly Progress Report to the Miami-Dade  
Board of County Commissioners Transportation and Aviation Committee**

Dear Chairman Moss:

I have enclosed for your information and use, the MIC Program Progress report for the period ending January 31, 2013.

As always, I look forward to working with you and the committee on this most important program. If you have any additional questions, please feel free to contact me at 305-470-5197.

Sincerely,

Gus Pego, P.E.  
District Secretary

Enclosure

C: L. Carl Filer, P.E., FDOT  
Ysela Llort, MDT  
Ric Katz, Kommunikatz, Inc.

**FIELD OFFICE**

3745 NW 25th Street  
Miami, Florida 33142


www.micmi.com  
1 888 838 5355

## Miami Intermodal Center



### MIAMI INTERMODAL CENTER (MIC) PROGRAM PROGRESS REPORT TO THE MIAMI-DADE COUNTY BOARD OF COUNTY COMMISSIONERS TRANSPORTATION AND AVIATION COMMITTEE

January, 2013  
(Volume 6, #2)

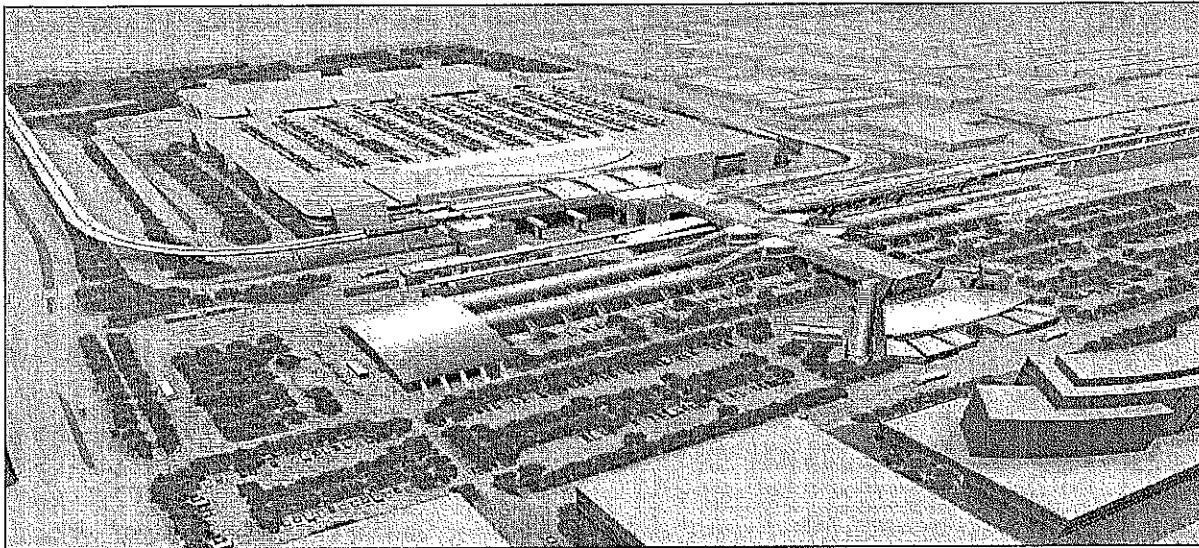

#### MIC Central Station

The following is the Monthly Status Report for work placed through January 31, 2013:

##### Rental Car Center (RCC)

- The Rental Car Center began Operations -- July 13, 2010
- All major elements of construction **have been completed**; The CO was issued March 8, 2011 and Final completion was achieved on May 16, 2011.
- The Rental Car Center was conveyed to Miami-Dade County per Quitclaim Deed dated December 20, 2011.

##### Rental Car Center (RCC) – Industry Meeting

- Beginning October 7, 2010 Bi-monthly meetings commenced with the Rental Car Companies; the next scheduled meeting is March 7, 2013. The bi-monthly industry meetings have transitioned from a construction meeting, conducted by FDOT, to operational meetings conducted by MDAD staff.

##### Roadways

- The Roadway Improvement Program has been completed.

### MIA Mover (APM) and MIC/MIA Station

- All construction of the MIC/MIA Station has been completed by Turner Construction. The CO was issued on January 20, 2011, and Final completion was achieved on January 24, 2011.

### Central Station Transit Hub

- The Department has provided 100% construction plans to Turner Construction for pricing and finalization of GMP#6C; GMP#6C negotiations were completed on May 16, 2011. Turner is in the process of obtaining permits from the Miami-Dade County Building Department. Turner Construction received the NTP on May 18, 2011, and construction officially began June 3, 2011. Construction is scheduled to be completed by December 2013. Turner to continue building construction, pile caps, utility and duct bank installations, roadway construction and sewer system.

### Landscaping

- Construction of the Landscaping on the LeJeune Road Corridor and the RCC has been completed.

### SFRTA (Tri-Rail)

- Due to the pending construction of the MIC Central Station, the SFRTA Board approved a relocation agreement with the Department on January 28, 2011, to cease operations at the Miami Airport Station, and resume those operations at the Hialeah Market Station. The Hialeah Market Place station will become the southern terminus of the SFRTA commuter rail system line, until the completion of the MIC Central Station in late 2013. Tri-Rail has ceased operations at Miami Airport Station as of September 12, 2011.

### Construction Schedule

- The current Summary Program Schedule is attached for your information and use. Below is the current construction milestones contained in that schedule.

Construction Projects	Start	Finish	Status
MIC/MIA Interchange & Le Jeune Road	FEB05	MAY08	COMPLETED
Temporary Tri-Rail Station		CANCELLED	
NW 21 <sup>st</sup> , 28 <sup>th</sup> & 29 <sup>th</sup> Streets	APR08	MAY09	COMPLETED
Rental Car Center	FEB07	JULY10	COMPLETED
MIA Mover MIC Station (FDO1)	FEB08	JAN11	COMPLETED
MIA Mover System (MDAD)	JAN09	SEPT 11	COMPLETED
MIA Mover MIA Station (MDAD)	JAN09	SEPT 11	COMPLETED
Metrorail Extension to MIC (MDT)	JAN09	JUL 12	COMPLETED
MIC Central Station	MAY11	DEC 13	UNDER CONSTRUCTION

Budget - Approved Program Budget is \$2.0 billion.

