Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float
PLANNING		1206		674	22-Mar-06 A	12-Nov-10	459
PLANNING		892		171	22-Mar-06 A	31-Aug-09	673
PLAN-010	DEVELOP PLAN OF ACTION FOR PLANNING WORK-FOR FTA	60	100%	0	22-Mar-06 A	26-Sep-06 A	
PLAN-020	MEETING WITH FTA TO REVIEW PLAN OF ACTION	0	100%	0		27-Sep-06 A	
PLAN-040	PREPARE FINAL PROJECT MANAGEMENT PLAN (PMP)	149	0%	149	05-Jan-09*	02-Jun-09	1031
PLAN-050	PREPARE PRELIMINARY REAL ESTATE ACQUISITION PLAN	149	0%	149	05-Jan-09*	02-Jun-09	1031
PLAN-060	PREPARE RAIL FLEET MANAGEMENT PLAN	239	0%	239	05-Jan-09*	31-Aug-09	941
PLAN-070	PREPARE BUS FLEET MANAGEMENT PLAN	239	0%	239	05-Jan-09*	31-Aug-09	941
PLAN-080	PREPARE QA PROGRAM PLAN	239	0%	239	05-Jan-09*	31-Aug-09	941
PLAN-030	PREPARE NEW STARTS/PE REQUEST PACKAGE	39	0%	39	30-Mar-09*	07-May-09	49
PUBLIC OUTREACH PROCESS		800		289	22-Mar-06 A	22-May-09	844
OUTR-010	PUBLIC OUTREACH PROCESS	1129	64.3%	403	22-Mar-06 A	22-May-09	1182
MPO LPA APPROVAL		179		179	10-Nov-08	16-Jul-09	381
PLAN 150	DEVELOP & ASSESS LOCALLY PREFERRED ALTERNATIVE	131	0%	131	10-Nov-08*	20-Mar-09	86
PLAN 110	Prepare Preliminary LPA Notices	5	0%	5	16-Feb-09	20-Feb-09	86
PLAN 120	Notices Approved By Marketing	5	0%	5	23-Feb-09	27-Feb-09	557
PLAN 130	Interagency Meeting to Present LPA	0	0%	0		23-Mar-09	533
PLAN 140	LPA Hearings & Meetings	114	0%	114	24-Mar-09	15-Jul-09	533
PLAN 160	MPO LPA APPROVAL (MPO Board Meeting)	0	0%	0		16-Jul-09	533
PREPARE NEWSTARTS/PE REQUEST PACKAGE TO FTA		0		0	13-May-09	13-May-09	35
NSPE-005	SUBMIT NEW STARTS/PE REQUEST PACKAGE TO FTA	0	0%	0		13-May-09	49
PREPARE SUPPLEMENTAL DEIS (SDEIS)		314		314	02-Feb-09	15-Apr-10	0
DEIS-010	PREPARE SDEIS	390	0%	390	02-Feb-09*	26-Feb-10	0
DEIS-020	SDEIS 45 DAY CIRCULATION & PUBLIC HEARING	46	0%	46	01-Mar-10	15-Apr-10	0
DEIS-030	SUPPLEMENTAL DEIS APPROVAL	0	0%	0		15-Apr-10	0
FINAL ENVIRON IMPACT STATEMENT (FEIS)		150		150	19-Apr-10	12-Nov-10	0
FEIS-010	RESPONSES TO COMMENTS	89	0%	89	19-Apr-10	16-Jul-10	0
FEIS-020	PREPARE FEIS	89	0%	89	19-Apr-10	16-Jul-10	0
FEIS-030	MDT REVIEW	40	0%	40	19-Jul-10	27-Aug-10	0
FEIS-040	FTA REVIEW	47	0%	47	30-Aug-10	15-Oct-10	0
FEIS-050	REVISE FEIS & RESUBMIT	26	0%	26	18-Oct-10	12-Nov-10	0
FEIS-060	FEIS APPROVAL	0	0%	0		12-Nov-10	0

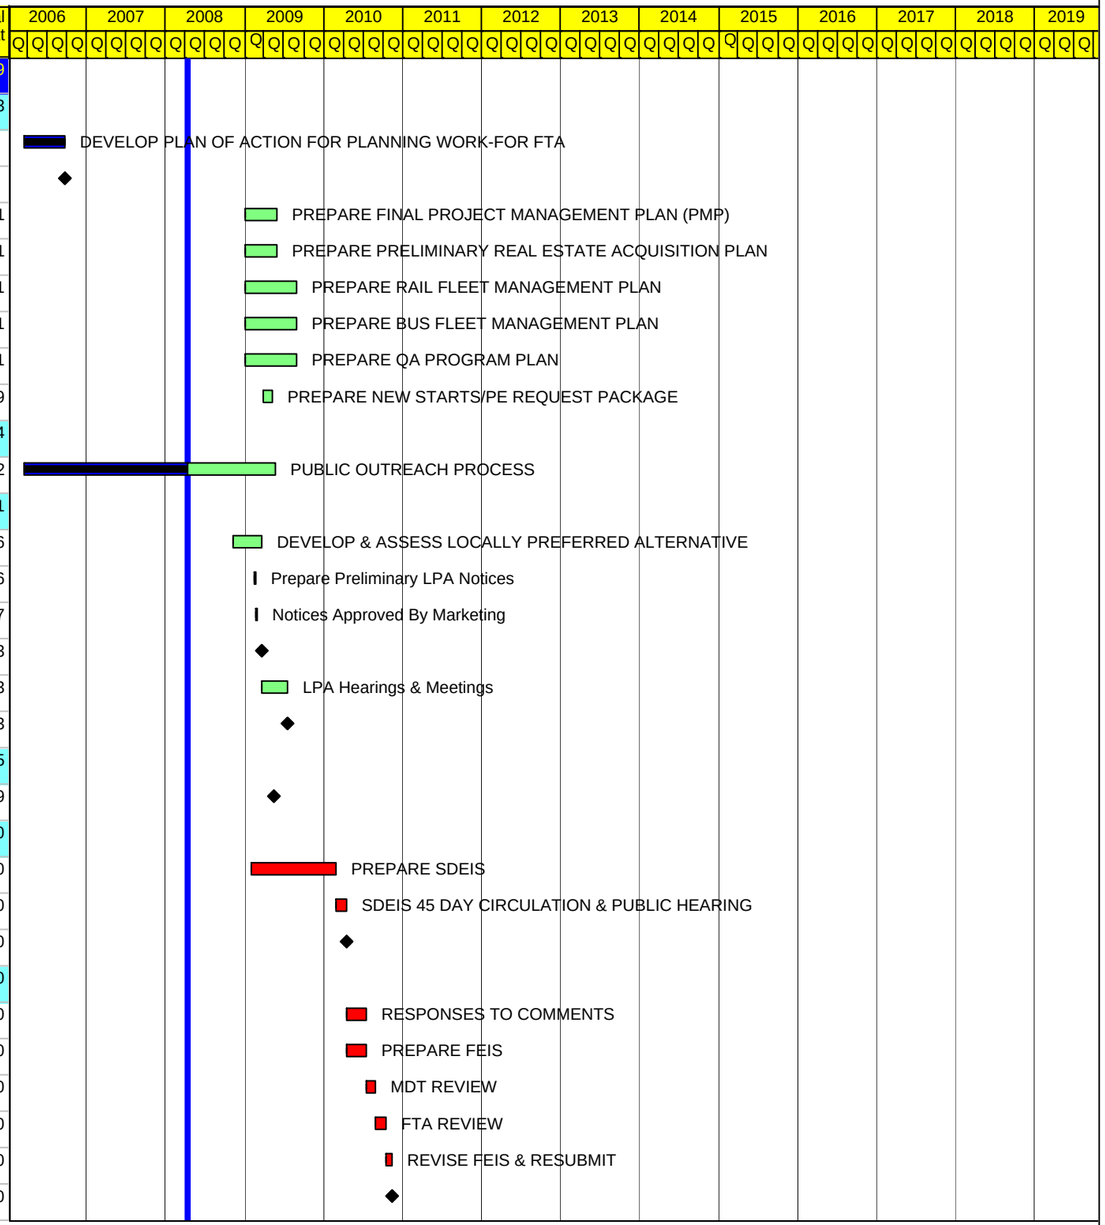

Start Date: 07-Aug-03
Finish Date: 17-Oct-19
Data Date: 15-Apr-08
Run Date: 30-Apr-08

Actual Work
Remaining Work
Critical Remaining Work
Milestone
% Complete

Filename: EW62

MIAMI-DADE TRANSIT (MDT) - MAJOR CAPITAL PROJECTS

ORANGE LINE PHASE 3: EAST-WEST CORRIDOR

PRELIMINARY MASTER PROJECT SCHEDULE

WORKING PROJECT SCHEDULE

April 2008 Schedule Update

Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float
DESIGN		950		950	30-Jan-10	20-Sep-13	657
PRELIMINARY ENGINEERING PLANNING/APPROVAL PROCES		205		205	30-Jan-10	12-Nov-10	209
PENG-010	PRELIMINARY ENGINEERING	287	0%	287	30-Jan-10	12-Nov-10	49
PENG-020	P.E. COST ESTIMATE	0	0%	0		14-Aug-10	384
NEW STARTS PE		260		260	01-Jan-11	31-Dec-11	0
NSPE-000	NEW STARTS PE	364	0%	364	01-Jan-11	30-Dec-11	0
NSPE-010	NSPE - 60% DESIGN & COST ESTIMATE-SEGMENT 1	0	0%	0	31-Dec-11		0
NSPE-020	NSPE - 60% DESIGN & COST ESTIMATE-SEGMENT 2	0	0%	0	31-Dec-11		0
NSPE-030	NSPE - 60% DESIGN & COST ESTIMATE-SEGMENT 3	0	0%	0	31-Dec-11		0
NSPE-500	SUBMIT NSPE - 60% COST ESTIMATE TO FTA	0	0%	0	31-Dec-11		0
FINAL DESIGN		646		646	01-Apr-11	20-Sep-13	566
FDCS-010	FINAL DESIGN CONSULTANT SELECTION-SEGMENT 1	295	0%	295	01-Apr-11	20-Jan-12	504
FDCS-020	FINAL DESIGN CONSULTANT SELECTION-SEGMENT 2	295	0%	295	01-Apr-11	20-Jan-12	549
FDCS-030	FINAL DESIGN CONSULTANT SELECTION-SEGMENT 3	295	0%	295	01-Apr-11	20-Jan-12	549
FDS1-010	FINAL DESIGN-SEGMENT 1	420	0%	420	28-Jul-12	20-Sep-13	315
FDS2-010	FINAL DESIGN-SEGMENT 2	420	0%	420	28-Jul-12	20-Sep-13	360
FDS3-010	FINAL DESIGN-SEGMENT 3	420	0%	420	28-Jul-12	20-Sep-13	360
FDTR-010	FINAL TRACK WORK DESIGN	420	0%	420	28-Jul-12	20-Sep-13	794
SYSTEMS DESIGN		458		458	20-Jul-11	19-Apr-13	767
SYS1-020	PREPARE SYSTEMS DESIGN,FURNISH,INSTALL SPECS	270	0%	270	20-Jul-11	14-Apr-12	1075
SYS1-030	SYSTEMS CONTRACTOR SELECTION(DESIGN,FURN,INST)	295	0%	295	29-Jun-12	19-Apr-13	1075
RIGHT-OF-WAY		686		686	26-Oct-12	12-Jun-15	0
		686		686	26-Oct-12	12-Jun-15	0
ROWA-120	RIGHT-OF-WAY ACQUISITION & UTILITY RELOCATION	960	0%	960	26-Oct-12	12-Jun-15	0
BID & AWARD		2840		1000	07-Aug-03 A	01-Aug-14	510
CONSULTANT SELECTION		2047		207	07-Aug-03 A	19-Jul-11	360
BIDA-010	PROGRAM MANAGEMENT CONSULTANT	584	100%	0	07-Aug-03 A	01-Jun-05 A	
BIDA-020	PLANNING CONSULTANT SELECTION (P.E. OPTION)	425	100%	0	01-Jan-04 A	17-Jan-05 A	
SYS1-010	SYSTEMS CONSULTANT SELECTION	290	0%	290	03-Oct-10	19-Jul-11	504
BID & AWARD - CONSTRUCTION		225		225	21-Sep-13	01-Aug-14	510
TRAC-010	TRACK WORK BID AND AWARD CYCLE	236	0%	236	21-Sep-13	14-May-14	794
BID1-010	BID AND AWARD CYCLE (PTP EXPEDITE)-SEGMENT 1	315	0%	315	21-Sep-13	01-Aug-14	315
BID2-010	BID AND AWARD CYCLE (PTP EXPEDITE)-SEGMENT 2	315	0%	315	21-Sep-13	01-Aug-14	360
BID3-010	BID AND AWARD CYCLE (PTP EXPEDITE)-SEGMENT 3	315	0%	315	21-Sep-13	01-Aug-14	360
AWAD-010	CONSTRUCTION CONTRACT AWARD-SEGMENT 1	0	0%	0		28-May-14	381
AWAD-020	CONSTRUCTION CONTRACT AWARD-SEGMENT 2	0	0%	0		28-May-14	426
AWAD-030	CONSTRUCTION CONTRACT AWARD-SEGMENT 3	0	0%	0		28-May-14	426
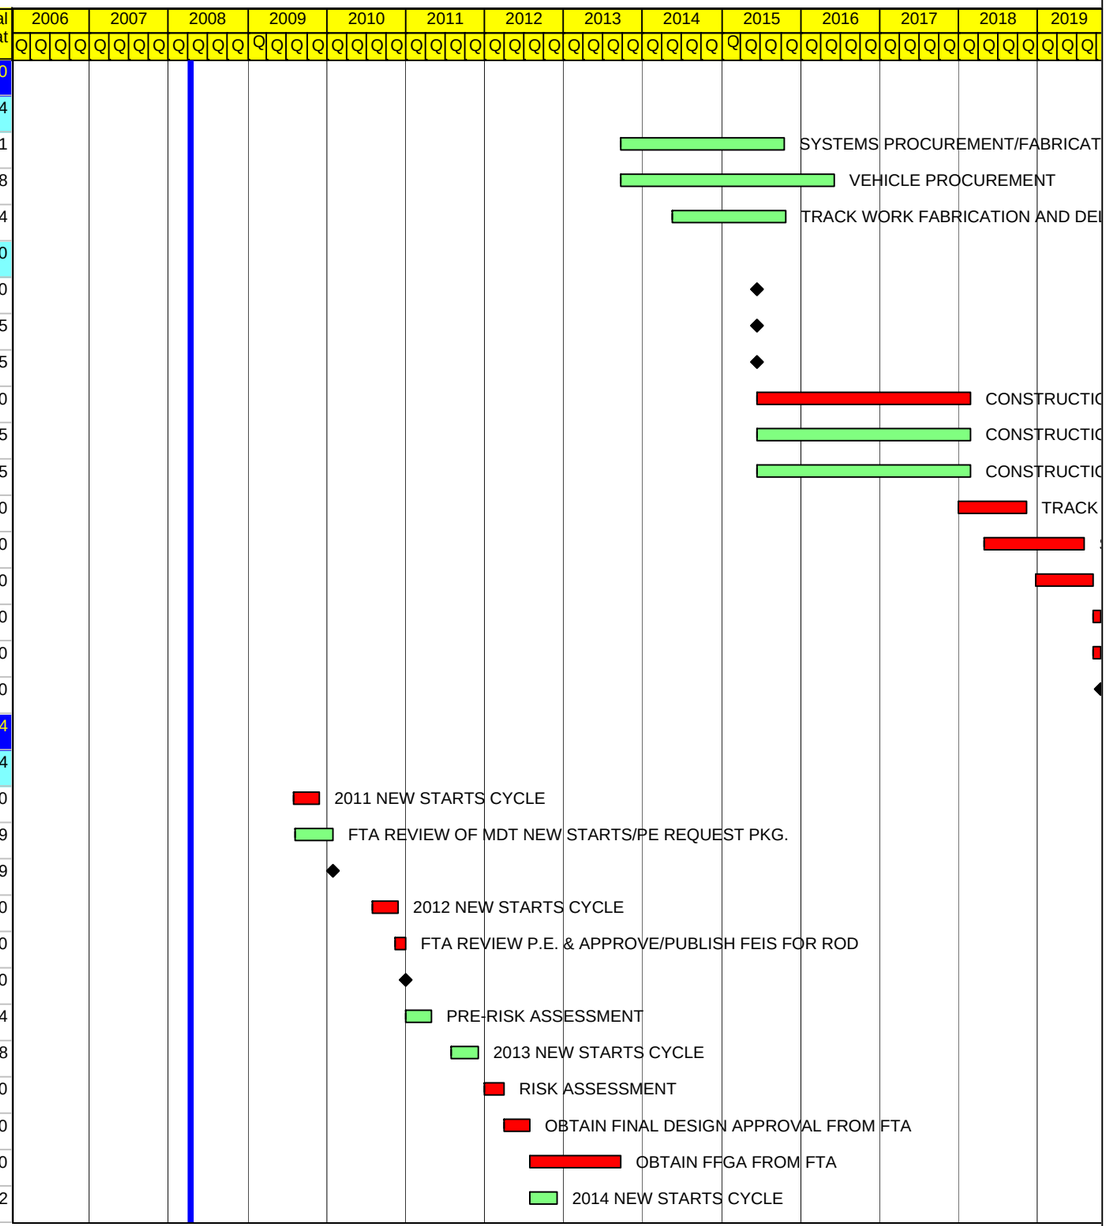
Activity ID	Activity Name	Original Duration	Activity % Complete	Remaining Duration	Start	Finish	Total Float
CONSTRUCTION		1584		1584	21-Sep-13	17-Oct-19	0
SYSTEMS, VEHICLES, & TRACK WORK PROCUREMENT		706		706	21-Sep-13	06-Jun-16	664
SYSI-010	SYSTEMS PROCUREMENT/FABRICATION	760	0%	760	21-Sep-13	20-Oct-15	921
VPRO-010	VEHICLE PROCUREMENT	990	0%	990	21-Sep-13	06-Jun-16	928
TRAC-020	TRACK WORK FABRICATION AND DELIVERY	530	0%	530	15-May-14	26-Oct-15	794
CONSTRUCTION		1134		1134	12-Jun-15	17-Oct-19	0
NTP1-010	NTP-SEGMENT 1	0	0%	0		12-Jun-15	0
NTP2-010	NTP-SEGMENT 2	0	0%	0		12-Jun-15	45
NTP3-010	NTP-SEGMENT 3	0	0%	0		12-Jun-15	45
CON1-010	CONSTRUCTION-SEGMENT 1	990	0%	990	13-Jun-15	26-Feb-18	0
CON2-010	CONSTRUCTION-SEGMENT 2	990	0%	990	13-Jun-15	26-Feb-18	45
CON3-010	CONSTRUCTION-SEGMENT 3	990	0%	990	13-Jun-15	26-Feb-18	45
TRAC-030	TRACK WORK INSTALLATION	316	0%	316	29-Dec-17	09-Nov-18	0
SYST-010	SYSTEMS INSTALLATION	462	0%	462	29-Apr-18	03-Aug-19	0
SYST-020	SYSTEMS TESTING	270	0%	270	22-Dec-18	17-Sep-19	0
SAFE-010	SAFETY CERTIFICATION	30	0%	30	18-Sep-19	17-Oct-19	0
TEST-010	PRE-REVENUE TESTING	30	0%	30	18-Sep-19	17-Oct-19	0
COMP-010	PROJECT COMPLETION	0	0%	0		17-Oct-19	0
FTA ACTIVITIES		1080		1080	01-Aug-09	20-Sep-13	1584
		1080		1080	01-Aug-09	20-Sep-13	1584
FTAA-050	2011 NEW STARTS CYCLE	122	0%	122	01-Aug-09*	30-Nov-09	0
FTAA-020	FTA REVIEW OF MDT NEW STARTS/PE REQUEST PKG.	172	0%	172	11-Aug-09	29-Jan-10	49
FTAA-025	FTA APPROVES START OF P.E.	0	0%	0		29-Jan-10	49
FTAA-060	2012 NEW STARTS CYCLE	122	0%	122	01-Aug-10*	30-Nov-10	0
FTAA-070	FTA REVIEW P.E. & APPROVE/PUBLISH FEIS FOR ROD	49	0%	49	13-Nov-10	31-Dec-10	0
FTAA-080	RECORD-OF-DECISION (ROD)	0	0%	0		31-Dec-10	0
FTAA-090	PRE-RISK ASSESSMENT	120	0%	120	01-Jan-11	30-Apr-11	244
FTAA-130	2013 NEW STARTS CYCLE	122	0%	122	01-Aug-11*	30-Nov-11	2878
FTAA-100	RISK ASSESSMENT	90	0%	90	31-Dec-11	29-Mar-12	0
FTAA-110	OBTAIN FINAL DESIGN APPROVAL FROM FTA	120	0%	120	30-Mar-12	27-Jul-12	0
FTAA-120	OBTAIN FFGA FROM FTA	420	0%	420	28-Jul-12	20-Sep-13	0
FTAA-140	2014 NEW STARTS CYCLE	122	0%	122	01-Aug-12*	30-Nov-12	2512
