

# Memorandum



**Date:** June 3, 2025

Agenda Item No. 2(B)(6)

**To:** Honorable Chairman Anthony Rodriguez  
and Members, Board of County Commissioners

**From:** Daniella Levine Cava *Daniella Levine Cava*  
Mayor

**Subject:** Miami-Dade Aviation Department: Aviation Capital Program Report – April 2025

## Most Recent News

This summer, the Miami-Dade Aviation Department (Aviation Department or MDAD) is moving forward with the bid and award phase for the construction of the North Terminal Gate Optimization Phase 1 & 2 and Infrastructure Upgrades projects at Miami International Airport (MIA). The project encompasses reconfiguring the existing aircraft gate layout for 18 gates (from D16 to D50) to accommodate new-generation aircraft, including the addition of jumbo gates at Concourse D. Modifications will also be made to the apron, utilities, and hold rooms servicing these gates. The project also involves the installation of new passenger boarding bridges (PBBs), PBB extensions, and the construction of additional fuel hydrant pits. Infrastructure enhancements required to support these projects include upgrades to the 400Hz and Pre-Conditioned Air (PC Air) systems to accommodate the new fleet mix. Substantial project completion is expected by late 2028.

## MIA's Modernization Program

As MIA continues to reach unprecedented heights in passenger and cargo growth, the modernization efforts underway to renovate 128 passenger boarding bridges, modernize 207 public-access restrooms, and improve 616 moving conveyance units (escalators, elevators and moving sidewalks) are not lagging. The new year began with ninety-five percent (95%) of the conveyances in operation as compared to 2024 when only eighty-five percent (85%) were functional. The remaining five percent (5%) are pending modernization, major repair or annual maintenance. Below are three (3) charts that show the progress being made with respect to MIA's conveyance units, public-access restrooms and passenger boarding bridges as of February 26, 2025.

### Moving Conveyances

	Total # of Units	Out-of- Service	Total # Under Construction	Total # Under Procurement	Renovations Completed
<b>Elevators</b>	<b>329</b>	<b>5</b>	<b>7</b>	<b>20</b>	<b>27</b>
<b>Escalators</b>	<b>191</b>	<b>*10</b>	<b>3</b>	<b>3</b>	<b>4</b>
<b>Moving Walkways</b>	<b>96</b>	<b>*17</b>	<b>8</b>	<b>8</b>	<b>2</b>
<b>Conveyance Units</b>	<b>616</b>	<b>32</b>	<b>18</b>	<b>31</b>	<b>33</b>

\*Notable Progress - Six (6) escalators were put into service, reducing the total number of out-of-service escalators from 16 to 10, and one (1) renovation was completed. One (1) moving

walkway was put into service, reducing the total number of out-of-service walkways from 18 to 17.

**Public-Access Restrooms**

	<b>Total # of Restrooms</b>	<b>Total # Under Construction</b>	<b>Total # Under Permitting</b>	<b>Total # Under Design</b>	<b>Renovations Completed</b>
<b>Public Access Restrooms</b>	<b>207</b>	<b>10</b>	<b>8</b>	<b>141</b>	<b>48</b>

Notable Progress - No change from previous month.

**Passenger Boarding Bridges (PBBs)**

	<b>Total # of PBB Units</b>	<b>*Out-of- Service</b>	<b>Total # Under Construction</b>	<b>Total # Under Procurement</b>	<b>Renovations Completed</b>
<b>PBBs</b>	<b>128</b>	<b>1</b>	<b>1 unit is being installed. 10 units are pending the “Notice to Proceed” (NTP)</b>	<b>14</b>	<b>32</b>

\*Notable Progress – One PBB was placed out-of-service as a replacement unit is being installed.

MDAD is making significant progress on its capital improvements portfolio which is set to transform Miami International Airport (MIA) through the construction of new terminals, concourses, ramps, runways, parking structures, restrooms, and hotels. A noteworthy project is the MIA Flamingo Garage Extension (Park 6) with substantial completion anticipated in January 2026. In addition, the design phase for the MIA Terminal Garages Exterior Cladding project is planned to commence this summer. More details on these initiatives can be found in sections entitled Significant Design Solicitations and Significant Projects in Construction further below.

**Background**

At the September 4, 2024, Board of County Commissioners (Board) meeting, Board members amended Ordinance No. 19-122 revising the reporting requirements of the monthly Aviation Capital Program Report (Report) and deleting the ratification requirement for all federal and state grants applied for or received including any amendments or supplemental agreements set forth in Section 2-285.2 of the Code of Miami-Dade County related to MDAD’s capital projects. The provisions of the adopted amendment require the inclusion of any information that highlights the improvements, infrastructure investments and capital projects at MIA in Miami-Dade in addition to any other relevant airport activities, accomplishments, and awards that contribute to making MIA a more efficient, innovative, and avant-garde airport. The amendment also requires that all federal or state grants (as described above) be included in the monthly Report, and as requested by Board members, it will also include all MDAD grant applications for the forthcoming year. As

such, in addition to the reporting requirements established under the authority of Ordinance No. 19-122 before it was modified, this new Report will include snapshots of any significant action steps taken or any major achievements that serve to enhance efficiencies, expand service offerings, modernize infrastructure, optimize operations or promote growth at MIA, and although not required by law, it will also include any action steps that further develop the County's General Aviation Airports (GAA), which include Miami-Opa locka Executive Airport (OPF), Miami Executive Airport (TMB), Miami Homestead General Aviation Airport (X51) and Dade-Collier Training and Transition Airport (TNT).

The action steps being implemented align with MIA's \$2 billion Modernization in Action Program that is currently underway. Over the next 5-7-years, this Program will continue to renovate and repair parking garages, passenger boarding bridges, public bathrooms, and the moving conveyance units. Additionally, it includes critical electrical and security upgrades. These improvements also complement the ongoing I AM MIA campaign, which is designed to enhance passenger loyalty and satisfaction through customer service training programs for the airport's 37,000 employees. Combined with a \$7 billion robust capital portfolio that funds the design and construction of new terminals, concourses, ramps, runways, parking facilities, restrooms, hotels, and more, these efforts will ultimately transform MIA into a future-ready, world-class, state-of-the-art airport.

In accordance with Ordinance 19-122 as amended, the Aviation Department has placed its fifty-third "Aviation Capital Program Report" on today's agenda. The new Report contains the additional content required by Ordinance No. 19-122 (as amended) to better inform residents, passengers, visitors, and Board members of the incremental action steps being taken by the County for MIA to achieve world class status and to further develop the GAA. Upon Board approval, a copy of the new Report will be posted on MDAD's webpage at [http://www.miami-airport.com/transparency\\_report.asp](http://www.miami-airport.com/transparency_report.asp) each month.

#### **April 2025 Report**

Table I, as depicted on the next page, shows MIA's calendar year-to-date passenger and cargo growth rates for the last five years including Year 2025 through the month of January. As can be seen, since the outbreak of the COVID-19 pandemic in March 2020, the percent increase in the total number of passengers from Year 2020 to Year 2021 totaled 99.86 percent as MIA experienced a strong recovery in the demand for air travel in 2021 while the demand for air cargo rose by approximately 18 percent, from 2.3 U.S. tons to 2.7 tons. From Year 2022 to Year 2024, the average percent increase in the total number of passengers totaled 10.3 percent and the same percent for total freight. These percent increases culminated in 2024, when MIA handled nearly 56 million passengers and more than 3 million U.S. tons of cargo.

No less significant are the passenger and total freight year-to-date numbers in 2025, which show that more than 5 million passengers traveled through MIA and nearly 272 thousand U.S. tons of total freight were registered in the month of January 2025. The unprecedented increases in the demand for air travel and air cargo traffic coupled with an upgrade from Fitch Ratings and Standard and Poor in January 2025 from A to A+ for financial strength and stability has positioned MIA for further growth.

**Table I - Calendar Year-to-Date (CYTD) Passenger and Cargo Growth Rates for Years 2020-2025**

	Year 2020	Year 2021	Year 2022	Year 2023	Year 2024	% Increase From 2022-2024	Year 2025 (Through January)
Total Passengers	18,663,858	37,302,456	50,684,396	52,340,934	55,926,566	10.3%	5,067,376
Total Freight	2,327,747	2,746,899	2,726,807	2,759,381	3,008,715	10.3%	271,048

It is worth noting that the increases in passenger and cargo traffic have led MIA to be recognized as one of the busiest airports in the United States. As shown in Table II below, in 2023, among U.S. airports, the Airports Council International (ACI) ranked MIA as the number 2 airport for international passengers, the number one in international freight and the number three airport in total cargo (freight and mail). Among airports worldwide, the ACI ranked MIA as the number six airport for international freight and the number 6 for total cargo (freight and mail).

For MIA to retain its competitive edge and continue to be recognized as a “Premier Passenger and Cargo Hub”, the successful implementation of MDAD’s capital portfolio that will renovate the airport’s Central, South and North Terminals and expand its cargo facilities is critical for MIA’s growth and future readiness as these development projects will replace aging and obsolete airport infrastructure and boost freight capacity. More importantly, these improvements will enable MIA to meet the growing demand of its passenger and cargo aviation markets and provide patrons with an enhanced, innovative, modern-day customer experience that offers greater value and optimizes convenience and efficiency.

**Table II - MIA Rankings for 2023**

<u>Among U.S. Airports</u>	<u>Among Worldwide Airports</u>
1 <sup>st</sup> International Freight	6 <sup>th</sup> International Freight
2 <sup>nd</sup> International Passengers	33 <sup>rd</sup> International Passengers
3 <sup>rd</sup> Total Cargo (Freight + Mail)	6 <sup>th</sup> Total Cargo (Freight + Mail)
3 <sup>rd</sup> Total Freight	6 <sup>th</sup> Total Freight
9 <sup>th</sup> Total Number of Operations	12 <sup>th</sup> Total Number of Operations
10 <sup>th</sup> Total Passengers	25 <sup>th</sup> Total Passengers

**Action Steps in Progress**

This new Report provides an outline of the action steps being put into effect to successfully implement \$7 billion of upgrades to modernize MIA and further develop the GAA, whether it is in the form of procurement solicitations, contract awards, large capital improvement projects that renovate terminals and concourses, or smaller but functional projects such as improvements to runways, taxiways, passenger loading bridges, gates, checkpoints, restrooms, baggage handling systems, parking facilities, etc., as well as any achievements, awards or high-tech investments that contribute to making MIA a more well-ordered, vanguard, future-ready airport. Below is a summary of the sub-programs within MDAD’s Capital Improvement Program (CIP) that will pave the way to meet passenger and cargo demand growth, which is projected to reach

approximately 77 million passengers and more than four (4) million tons of freight by the year 2040. These action steps also include \$1.7 billion in maintenance upgrades over the next 10 years.

- Central Terminal Redevelopment
- Concourse “F” Modernization
- North Terminal Redevelopment
- South Terminal Expansion (New Concourse K)
- Expanded Cargo Aircraft Parking Positions & Cargo Handling Facilities
- New Privately Funded Airport Hotel

**A. Contracts Awarded by the Board in 2025 through January 2025**

**1. January 22, 2025**

- a) Contract Award to Leidos, Inc.; Contract No. EVN0000402. The Scope of Work provides for the purchase of screening equipment for the Transportation Security Administration (TSA), which will be used to expand and modernize TSA’s security screening operations throughout MIA, beginning with the new Concourse F and Concourse D checkpoints which are the first to be delivered per this project’s schedule. (\$35,878,426.00)
- b) Ratification of Contract Award to TK Airport Solutions, Inc.; Emergency Contract No. E-10395. The Scope of Work provides for a one-year and six-month term for the removal and installation of passenger boarding bridges at MIA Gate D23. (\$537,670.00)

**2. February 4, 2025**

- a) Ratification of Five (5) Emergency Contract Awards to HNTB Corporation; (E-10381) Professional Service Industries, Inc.(E-10382); TY Lin International, Inc.(E-10383); CMC Contractors, LLC. (E-10417; Bliss & Nyitray, Inc.(E-10476). The Scope of Work involves structural repairs to the Automated People Mover (APM) Skytrain in the North Terminal. (\$7,833,045.99)
- b) Contract Award to Allied Contractors, Inc.; Contract No. AC001A. The Scope of Work provides construction services at MIA to build a new airside-operating-area (AOA) access gate and all associated facilities to service MIA’s central base area including air conditioning, bathrooms, backup generators, canopy, bollards, a gate arms system, bus shelters on both sides of the gate facility, as well as the communication infrastructure required. The primary function of the gate will be to facilitate access to construction activities during the implementation of MDAD’s CIP. (\$8,755,384.00)
- c) Ratification of Two (2) Contract Awards to N&K Enterprises, Inc. (FB01166) and SFM Services, Inc.(FB01167). The Scope of Work provides for the purchase of janitorial services to ensure the continuity of services while the County completes the reprocurement for locations that include mainly non-terminal MDAD buildings and the General Aviation Airports (GAA). (\$3,540,172.00)

**3. February 22, 2025**

- a) Contract Award to Globe Facilities Management, Inc.; Contract No. EVN0000201. The Scope of Work provides for the provision of janitorial services for a 5-year term at MIA’s non-terminal buildings including, but not limited to, public and employee parking garages, maintenance buildings, Miami Intermodal Center (MIC), rental car

- center, and other MIA properties identified as Area B in the solicitation. (\$24,360,999.00)
- b) Contract Award to SFM Services Inc.; Contract No. EVN0000201. The Scope of Work provides for the provision of janitorial services for a 5-year term at MIA's non-terminal buildings including, but not limited to, cargo buildings, County's administrative offices, other outlying buildings at MIA, and the four General Aviation Airports (GAA) identified as Area C in the solicitation. (\$34,516,333.00)
  - c) Rejection of all bids received in connection with Area A of Contract No. EVN0000201, directing the County Mayor to negotiate contracts with ABM Aviation to provide janitorial services to the MIA terminal and landside areas and with Flagship Aviation Services, LLC for the airside areas, and to bring the recommendation before the full Board within 30 days.

Summary of Contracts Awarded by the Board in 2024

1. March 5, 2024  
Contract Award to TK Airport Solutions, Inc.; Contract No. ITQ-MDAD-67621-JM. (\$15,290,198.40)
2. April 2, 2024  
Contract Award for a Professional Services Agreement for General Civil Engineering Services to Premiere Design Solutions, Inc.; Contract No. E22-MDAD-04, Phase 1. (\$3,717,303.00)
3. June 4, 2024
  - a) Contract Award for a Professional Services Agreement for General Civil Engineering Design Services to AtkinsRéalis USA, Inc.; Contract No. E23AV02C (\$6,616,500.00)
  - b) Contract Award for a Professional Services Agreement for General Civil Design Engineering Services to T.Y. Lin International; Contract No. E23AV02B - same as above.
  - c) Contract Award for a Professional Services Agreement for General Civil Engineering Design Services to EXP U.S. Services, Inc.; Contract No. E23AV02A- same as above.
4. June 18, 2024  
Contract Award to Hotelzo LLC d/b/a Wait N Rest; Contract No. EVN0000237. (\$10,000,000.00)
5. July 2, 2024  
Contract Award for a Professional Services Agreement for General Civil Engineering Design Services to Burns & McDonnell Engineering Company, Inc.; Contract No. E23AV01. (\$5,513,750.00)
6. October 16, 2024
  - a) Contract Award for a Professional Services Agreement for General Civil Engineering Design Services to Carty Architecture, LLC; Contract No. A23AV02. (\$39,878,678.00).
  - b) Construction Contract to rehabilitate MIA's Concourse E Satellite Automated People Mover (APM) Bridge to Magnum Construction Management, LLC; Contract No. AB003A. (\$13,303,175.00)
  - c) Construction Contract to rehabilitate MIA's South Terminal Concourse H to Magnum Construction Management, LLC; Contract No. AA018B. (\$11,040,790.25)
  - d) Contract Award to manage, operate and maintain airport-owned fueling systems to Allied Aviation Fueling of Miami, Inc.; Contract No. EVN0000425. (\$6,263,791.00)

7. December 3, 2024

- a) Contract Award for a Professional Services Agreement to Gannett Fleming, Inc.; Contract No. E23AV04. (\$5,513,750.00).
- b) Contract Award for a Professional Services Agreement to Hazen & Sawyer, PC; Contract No. E23AV03. (\$2,205,500.00).
- c) Contract Award for a Professional Services Agreement to Adelte Ports & Maritime S.L.U.; Contract No. EVN0008106. (\$21,554,110.54)

**B. Maintenance Contracts Awarded by the Board in 2025 through January 2025**

1. January 22, 2025

Resolution No. 1090-23 provides for the implementation of certain projects identified in connection with a Master Service Agreement with Florida Power and Light (FP&L) for Building 3090 at MIA, which provides for resilient infrastructure, sustainability and electrical vehicles for a 20-year term with automatic renewals, totaling approximately \$64,737.42 to \$77,684.90 over the 20-year period.

Summary of Maintenance Contracts Awarded by the Board in 2024

July 2, 2024

Contract Award for repair and maintenance services to Evolution Elevator & Escalator Company and Otis Elevator Company; Contract No. EVC0003576. (\$10,385,000.00)

**C. Development Lease Agreements Awarded by the Board in 2025 through January 2025 - None**

Summary of Development Lease Agreements Awarded by the Board in 2024

1. January 17, 2024

Development Lease Agreement with Reliance Aviation Miami, LLC (Reliance) - Minimum Investment Amount: \$6,000,000.00.

2. July 16, 2024

a) Development Lease Agreement with Ocean Aviation TMB, LLC (Ocean Aviation) – Minimum Investment Amount: \$67,200,000.00.

b) Master Development and Lease Agreement with Miami Gateway Partners, LLC- (Miami Gateway) –Minimum Investment Amount: \$400,000,000.00

3. September 17, 2024

Development Lease Agreement with KTMB Acquisitions, LLC (KTMB) –Minimum Investment Amount: \$14,750,000.00.

**D. Contracts for Sale & Purchase Awarded by the Board in 2025 through January 2025 - None**

Summary of Contracts for Sale & Purchase Awarded by the Board in 2024

1. October 16, 2024

Contract for Sale & Purchase between the County (Buyer) and Caracol Developers, LLC, (Sellers) - \$15,900,000.00.

2. December 3, 2024

Contract for Sale & Purchase between the County (Buyer) and MIA at 25<sup>th</sup> Street LLC (Sellers) - \$17,000,000.00.

**E. Significant Design Solicitations**

**Notice to Professional Consultants (NTPC)**

1. MIA Dolphin/Flamingo & New Parking Garage 6 Exterior Cladding (AC053A) – The Scope of Work involves the procurement of an exterior screen system that will act as an aesthetic skin enhancing the highly visible parking garages and their facades. The NTPC was advertised on August 2, 2024, and the proposals that were received on September 10, 2024. The first-tier evaluation meeting was held on November 20, 2024; the negotiation phase is underway through February 2025.
2. MIA Central Terminal Redevelopment Phase II (V008C) – The Scope of Work involves expansion of the queuing areas between Concourses E and F to provide new passenger circulation space as well as new TSA checkpoints. The NTPC was advertised on September 16, 2024, and the project briefing took place on September 23, 2024; Requests for Information (RFIs) were due on September 30, 2024, and the proposals received on October 30, 2024, are undergoing the evaluation process. The second-tier evaluation meeting took place on February 7, 2025.
3. MIA Cc. Low E and E Satellite Mechanical and Electrical Rooms Upgrade (CA010A) – The scope of work involves upgrading the Mechanical and Electrical rooms in Lower Cc, E, and E-Satellite (all levels). This includes replacing equipment, making necessary room adjustments to fit new equipment, and retrofitting existing equipment to meet current code compliance. The NTPC is anticipated to be advertised in March 2025.

**Request for Design-Build Services (RDBS)**

4. MIA South Terminal Expansion East (X078A) – This project includes a three-level expansion of the South Terminal to the east of Concourse J. The project will provide six (6) domestic narrow-body aircraft gates and increase post-security concessions space. The RDBS was issued on April 23, 2024, and the Step II presentations took place on December 18, 2024. It is anticipated that negotiations will be completed in May 2025.

**F. Significant Projects in Design**

1. MIA Fuel Storage Facility Expansion (W019A): The Scope of Work provides for the construction of a new jet fuel storage tank facility and the associated components. Completion of Design Documents – September 2025. (Overall Total Project Costs: \$39,200,000.00)
2. MIA Concourse F to H Sterile Connector, Third Level (CA004A): The Scope of Work provides for secure and sterile connectivity between Concourses F to H through an interconnector that will improve efficiencies in security checkpoints, passenger circulation areas and airline operations. Completion of Design Documents – February 2026. (Overall Total Project Cost: \$96,600,000.00)



3. MIA Central Terminal Concourse F Baggage Handling System (BHS) New Piers and Cross Over South to Central Terminal (DA076A): The Scope of Work for this design-build project includes the implementation of four (4) new piers in the Central Terminal and a new baggage handling system crossover from the South Terminal to the Central Terminal that will improve the capacity of the existing outbound system. Completion of Design Criteria Package – August 2025. (Overall Total Project Cost: \$28,900,000.00)
4. MIA Perimeter Hardening Phase I (AB016A): The Scope of Work consists of the replacement of the existing Airside Operating Area (AOA) fence with a new MDAD Design Guideline Standard AOA high security fence. Completion of Design Documents – December 2025. (Overall Total Project Cost: \$32,700,000.00)
5. MIA Central Terminal Redevelopment Phase I (BA061A) – The Scope of Work consists of a four-level building expansion to include a post-security corridor and additional concessions between Concourse E and Concourse F. The design documents phase began in December 2024 and is expected to be completed in July 2027. (Overall Total Project Cost: \$373,000,000.00)
6. MIA Central and South Terminal Bag Claim Optimization Phase II (BA059A): The scope of work consists of the design, supply, and installation of new claim devices in the Central and South Terminals of MIA. Completion of Design Documents – April 2025. (Overall Total Project Cost: \$18,400,000.00)
7. MIA NTD Baggage Handling System Modifications to the Inline CBIS (AB040A): The scope of work entails upgrades to the existing Transportation Security Agency (TSA) screening equipment within the North Terminal baggage handling system. Completion of Design Documents – November 2025. (Overall Total Project Cost: \$18,200,000.00)
8. MIA North Terminal Gate Optimization Phase I & II (AB048A): The scope of work includes reconfiguration of the existing aircraft gate layout to accommodate new generation aircraft at Concourse D. Completion of Design Documents – June 2025. (Overall Total Project Cost: \$29,900,000.00)

**G. Significant Construction Solicitations**

**Requests to Advertise(RTA)/Requests for Quotes(RFQ)/Requests for Proposals(RFP)**

1. MIA Central Base Airside Operations Area (AOA) Construction Gate (AC001A): The Scope of Work provides for the construction of a new AOA access gate to service MIA's central base area. The RTA was issued on August 7, 2024, and proposals were due in October 2024, the award recommendation is in process. (Overall Total Project Costs: \$13,400,000.00)
2. South Terminal Concourse J Federal Inspection Service (FIS) Checkpoint Upgrade/Refurbishment (BA057A): The Scope of Work provides for the improvement of the passenger processing capacity for various security checkpoints in the South Terminal, which are currently undergoing upgrades to meet the present and future demands of passengers. The RTA was issued on August 15, 2024, and proposals were received in September 2024. The award recommendation is in process. (Overall Total Project Costs: \$3,800,000.00)

3. MIA Satellite E New Chiller Plant (Project No. U010D-I): The Scope of Work involves the construction of a modular type building to house two (2) new centrifugal water-cooled chillers with a total net peak load refrigeration capacity of 1,050 tons. The RFP was issued on September 6, 2024, and proposals were received on January 15, 2025. The award recommendation is in process. (Overall Total Project Costs: \$38,700,000.00)
4. MIA Bridge Rehabilitation (AB003B): The Scope of Work addresses multiple deficiencies identified in the Bridge Inspection Report dated April 2022, which was prepared by the Florida Department of Transportation (FDOT). It is anticipated that the RTA will be issued in March 2025. (Overall Total Project Costs: \$18,800,000.00)
5. MIA North Terminal D2 Checkpoint Upgrades (AC088A): The Scope of Work provides the infrastructure and support needed to replace (4) existing x-ray machines with (3) full size automated screening lanes, as well as one (1) mid-size screening lane to increase the throughput capacity. The RTA was issued on October 31, 2024, the pre-bid meeting was held on November 14, 2024, and the bid opening took place on December 12, 2024. The award recommendation process is ongoing. (Overall Total Project Costs: \$1,400,000.00)
6. MIA Airports Operation Center (P250A): The Scope of Work involves combining the functions of MIA's Airport Operations Center and Emergency Operations Center to provide a more efficient and unified control center. The RTA was issued on January 10, 2025, the pre-bid conference took place on January 31, 2025, and the bid opening is scheduled for the end of March 2025. (Overall Total Project Costs: \$35,000,000.00)
7. MIA Concourse J Gates Advanced Visual Guidance Detection System (VGDS) (V100A): The Scope of Work involves the procurement of 17 Advanced Visual Guidance Detection System displays and operator panels for installation at 17 gates in Concourse J, Gates J-2 through J-18. The RTA is anticipated to be issued in March 2025. (Overall Total Project Costs: \$8,200,000.00)
8. MIA Concourse H Visual Guidance Detection System (VGDS) (T012A-1): The Scope of Work includes the procurement of VGDS displays and operator panels for installation at MIA Concourse H gates. The RTA is expected to be issued in March 2025. (Overall Total Project Costs: \$8,900,000.00)
9. Demolition and Replacement of Building No. 3032, New Building and Tenant Relocations (AB041A): The Scope of Work provides for the construction of a two-story building approximately 51,200 square feet in size. The RTA is anticipated to be issued in March 2025. (Overall Total Project Costs: \$35,600,000.00)
10. MIA RIM Hot Spot No. 4 (Corral Area) (Y118A): The Scope of Work consists of the reconfiguration of MIA's Corral pavement, reconfiguration of taxiway connectors, and construction of crossover taxiway pavements and a new exit required to comply with the recommendations of the most recent Federal Aviation Administration (FAA) Advisory Circular Airport Design. The RTA is expected to be issued in March 2025. (Overall Total Project Cost: \$101,100,000.00)

**H. Significant Projects in Construction**

1. MIA Baggage Handling System (BHS) Central Terminal to South Terminal Crossover (T042B): The Scope of Work includes the design, permit, and installation of a new

- baggage cross-over conveyor line from the Central Terminal to the South Terminal, as well as the implementation of the crossover automated tag readers to significantly enhance pier capacity in the South Terminal BHS. The Notice to Proceed was issued on January 30, 2023; Estimated Project Completion: August 2025. (Overall Total Project Costs: \$5,200,000.00)
2. MIA Lower Concourse E, E-Satellite Stucco, Paint, Lightning, and Visual Guidance Detection System (AA005A): The Scope of Work involves stucco replacement, exterior painting, lightning protection, and the installation of ten (10) Type 2 Visual Guidance Detection System displays at MIA. The Notice to Proceed Date was issued on May 16, 2023; Estimated Project Completion: July 2025. (Overall Total Project Costs: \$25,000,000.00)
  3. MIA Central Terminal Ticket Counters, Conveyors and K-1 Doors for Ticket Counters (TC) TC12-TC17 (V043A): The Scope of Work consists of remodeling the existing ticket counters to accommodate airline needs and modernize the terminal. The Notice to Proceed Date was issued on December 4, 2023; Estimated Project Completion: June 2025. (Overall Total Project Costs: \$23,500,000.00)
    - a. POD No.2 (TC#14 & TC#15): Construction Commencement – December 2023; Project Completion - August 2024; Temporary Certificate of Occupancy (TCO) was obtained September 12, 2024.
    - b. POD No.1 (TC#16 & TC#17): Construction Commencement - September 2024; TCO was obtained on February 20, 2025.
    - c. POD No.3 (TC#12 & TC#13): Construction Commencement – February 2025; Estimated Project Completion – May 2025.
  4. MIA Employee Parking Garage, Park 6 (V042A): The Scope of Work includes the construction of a seven-level parking structure with 2,240 parking spaces including two vehicular/pedestrian connections per level to the Flamingo Garage. The Notice to Proceed Date was issued on January 16, 2024; Estimated Project Completion: January 2026. (Overall Total Project Costs: \$137,000,000.00)
  5. MIA Concourse F Refurbishment Checkpoint Relocation, Demolition (V008F-1): The Scope of Work consists of repairs and upgrades to MIA Concourse F, including selective demolition of interior finishes and mechanical, electrical, and plumbing systems within the Concourse to accommodate a new Transportation Security Administration (TSA) checkpoint that will be constructed in a subsequent construction phase. The Notice to Proceed was issued on August 12, 2024; Estimated Project Completion: April 2025. (Overall Total Project Costs: \$1,900,000.00)
  6. MIA Concourse F Refurbishment Checkpoint Relocation, Finishes (V008F-2): The Scope of Work consists of remodeling a concession area located on the second level of Concourse F to house a new Transportation Security Administration (TSA) checkpoint area. The Notice to Proceed was issued on August 12, 2024; Estimated Project Completion: February 2026. (Overall Total Project Costs: \$ 8,380,000.00)
  7. OPF Blast Fence (X005A): The Scope of Work consists of the installation of the blast fence including the foundations and all structural requirements at Miami Opa-Locka

- Executive Airport (OPF). The Notice to Proceed was issued on August 12, 2024; Estimated Project Completion: July 2025. (Overall Total Project Costs: \$2,400,000.00)
8. OPF Engine Run-Up Pad (X010A): The Scope of Work includes the development of run-up pad at OPF. The Notice to Proceed was issued on August 19, 2024; Estimated Project Completion: January 2026. (Overall Total Project Costs: \$7,300,000.00)
  9. MIA Concourse F Refurbishment F-4 Hold Room Structural Repairs and F4, F6 & F8 Rehabilitation (V008F-3): The Scope of Work includes interior upgrades and structural repairs at Gates F4, F6 and F8 in Concourse F. The Notice to Proceed was issued for November 18, 2024; Estimated Project Completion: November 2025. (Overall Total Project Costs: \$3,400,000.00)
  10. MIA Parking Garage (Dolphin/Flamingo) Repairs & Upgrades Phase 1A (D105C-IA): The Scope of Work includes electrical and structural repairs throughout the Dolphin and Flamingo Garage structures as identified on a 40-year Recertification Inspection Report. The Notice to Proceed was issued for September 21, 2023; Estimated Project Completion: March 2025. (Overall Total Project Costs: \$11,800,000.00)
  11. MIA Building No. 3032 Demolition (AB041A-1): The Scope of Work provides for the demolition, remediation, and abatement of an existing two-story building at MIA. The Notice to Proceed was issued for February 24, 2025; Estimated Project Completion: October 2025. (Overall Total Project Costs: \$4,000,000.00)

#### **I. Federal Grants & Amendments**

Table III consists of grant applications that were submitted to the Federal Aviation Administration (FAA) in June 2024 and awarded and fully executed in July and August 2024. The funding sources include Airport Terminal Program (ATP), Airport Infrastructure Grant (AIG), and Airport Improvement Program (AIP) grant funds.

Table III – Federal Grant Applications Submitted to the FAA

<b>Project Title</b>	<b>Funding</b>	<b>Grant Amounts</b>
<b>New FAA Grants</b>		
MIA Central Terminal Redevelopment Phase 1 – Design	ATP	\$15,000,000.00
MIA Central Terminal E-F Demolition – Design	AIG	\$4,695,541.00
MIA Concourse E Satellite APM Bridge Rehabilitation – Construction	ATP	\$8,560,000.00
MIA Central Base Apron Rehabilitation Phase 3 – Construction	AIP	\$6,859,878.00
MIA Fuel Storage Facility Expansion – Design	AIG	\$1,602,437.00
MIA North Terminal Public Restrooms Modernization Phase A1 – Construction	AIG	\$2,493,035.00
South Terminal Concourse H Rehabilitation - Construction	AIG	\$5,000,000.00
MIA F-H Interconnector - Design	AIG	\$2,821,090.00

MIA Concourse F Refurbishment – (V008F-1 thru 3) Construction	AIG	\$4,556,522.00
TMB Proposed New ADG III North Apron Taxilane & Access Road - Design	AIG & AIP	\$790,577.00
OPF Runway Incursion Mitigation Hot Spot 3 - Design	AIG & AIP	\$654,423.00

**J. State Grants and Amendments**

Table IV consists of Florida Department of Transportation (FDOT) grant applications and amendments that were submitted to FDOT in June 2023 and awarded and fully executed through Public Transportation Grant Agreements (PTGAs) in July, August and September 2024. The funding sources include Aviation Grant Program (AGP) and Intermodal Development Program (IDP) grant funds.

Table IV – State Grant Applications Submitted to FDOT

<b>Project Title</b>	<b>Funding</b>	<b>Grant Amount</b>
<b>Amendments to PTGAs for Additional Funding</b>		
MIA Airport Operations Control Center – Design & Construction	AGP	\$2,393,910.00
MIA Terminal Wide Re-roofing – Design & Construction	AGP	\$2,349,345.00
MIA Intermodal Center – Property Management	IDP	\$80,498.00
<b>New PTGA Agreements</b>		
MIA Perimeter Rd Bridge Replacement – PD&E Study	AGP	\$480,785.00
MIA Passenger and TNC Remote Parking Lot – Design & Construction	AGP	\$3,000,000.00
MIA Cybersecurity Systems and Plan	AGP	\$1,562,500.00
MIA Terminal Wide Public Restrooms Modernization	AGP	\$1,000,000.00
MDAD GAA Airports Taxiways and Apron Rehabilitation, Restoration and Repairs – Design & Construction	AGP	\$500,000.00
OPF Runway Incursion Mitigation 03 – Construction	AGP	\$662,880.00
MIA Runway Incursion Mitigation Hot Spot 04 – Construction	AGP	\$5,500,000.00
TMB Proposed New ADG III North Taxilane at Lot 16 and Access Road - Construction	AGP	\$1,000,000.00
MIA South Terminal Expansion East - Terminal Hardstand & GSE Facility – Design & Construction	AGP	\$5,490,254.00
OPF 09L/27R Runway Rehabilitation - Pavement and Lighting - Construction	AGP	\$2,000,000.00

**K. Future Federal Grant Applications (Fiscal Year 2025)**

Table V consists of grant applications submitted to the FAA on October 1, 2024, based on project cost estimates. These applications will be resubmitted to the FAA on June 1, 2025, with the final negotiated design contract award amounts and/or the final bid construction contract award amounts.

These finalized grant applications will be reviewed by FAA and grant awards will be issued between the months of July 1, 2025, and August 31, 2025, except for those projects using discretionary funds, which are not guaranteed to receive grant funds until the FAA issues a formal grant award notification. The funding sources include Airport Terminal Program (ATP), Airport Infrastructure Grant (AIG), and Airport Improvement Program (AIP) grant funds.

Table V – Fiscal Year 2025 Federal FAA Grant Applications

<b>FY2025 FAA APPLICATIONS</b>		
<b>Project Name</b>	<b>Funding</b>	<b>Grant Amount</b>
MIA South Terminal Expansion – Design-Build	ATP - Discretionary Funds	\$35,000,000.00
MIA South Terminal Expansion – Design Build	AIG	\$56,245,932.00
MIA Runway Incursion Mitigation Hot Spot 4 – Construction	AIP	\$24,836,354.00
MIA Runway Incursion Mitigation Hot Spot 4 - Construction	AIP - Discretionary Funds	\$37,556,587.00
MIA Runway Incursion Mitigation Hot Spot 4 - Construction	AIG	\$10,515,789.00
MIA Bridge Rehabilitation - Construction	AIG	\$12,944,636.00
TMB Apron Taxilane H Eastward Extension Expansion – Construction. Project was deferred to FY2026 for additional grant funding	AIG	\$564,000.00
TMB Apron Taxilane H Eastward Extension Expansion – Construction. Project was deferred to FY2026 for additional grant funding	AIP	\$2,735,803.00
TMB Apron Taxilane H Eastward Extension Expansion – Construction. Project was deferred to FY2026 for additional grant funding	AIP - Discretionary Funds	\$7,432,103.00
OPF Runway Incursion Mitigation 20 - Design	AIG	\$295,000.00
OPF Runway Incursion Mitigation 20 - Design	AIP	\$150,000.00
OPF Runway Incursion Mitigation 20 - Design	AIP - Discretionary Funds	\$828,000.00

Exhibit A displays a series of photographs that tell MIA's transformation story as it unfolds. Each month, various pictures will be posted according to the MDAD projects that are approved, initiated or completed, furthermore, photos of any action steps, awards, achievements or events that contribute to MIA's transfiguration or that further develop the GAA will also be included. This month, the pictures include the January 2025 I AM MIA Reward and Recognition event; various innovative and maintenance projects; and the televised press conference hosted by Mayor Daniella Levine Cava at MIA on February 24, 2025, which was attended by more than 100 airport partners and employees to celebrate the airport's record-breaking passenger and cargo growth in 2024, the upgrade from Fitch Ratings and Standard and Poor from A to A+, and the continued success of the Modernization in Action Program and MDAD's CIP, which together are repairing and refurbishing MIA's moving conveyances, public-restrooms, passenger boarding bridges as well as expanding and renovating terminals, concourses, ramps, runways, parking facilities, and hotels. These modernization projects will ultimately transform MIA into a future-ready, world-class, state-of-the-art airport.

In compliance with the reporting requirements of Ordinance No. 19-122 before it was amended, Exhibit B provides the status of the capital projects procured and awarded under the seal of the Ordinance including the estimated contract values, the project qualifications for award and the proposed contract measures. Exhibit C provides the financial status of MDAD's capital projects including detailed project budget information, project expenditures from the time a contract is awarded through project completion, and indicators that flag when project expenditures reach 30 percent, 60 percent, and 90 percent of the approved budget amount. The Summary of Changes shows the differences between the previous month's report (March 2025) and the current month's report (April 2025) facilitating review of the most recent actions.

Pursuant to Ordinance No. 14-65, this memorandum will be placed on a Board agenda for review within 30 days.

Should you have any questions or require additional information, please contact Aviation Director, Ralph Cutié, at 305-876-7066.



---

Jimmy Morales  
Chief Operating Officer

C: Geri Bonzon-Keenan, County Attorney  
Gerald Sanchez, First Assistant County Attorney  
Jess McCarty, Executive Assistant County Attorney  
Office of the Mayor Senior Staff  
Ralph Cutié, Director, Miami-Dade Aviation Department  
Basia Pruna, Director, Clerk of the Board  
Yinka Majekodunmi, CPA, Commission Auditor  
Eugene Love, Agenda Coordinator





# EXHIBIT A

April 2025



FUTURE  READY





## I AM MIA Reward & Recognition Event January 2025



MIA Director and CEO Ralph Cutié recognized Landside Operations Officer Norbert Bielecki and Department of Homeland Security (DHS) Officer Adrian Powell as the R&R winners for January 2025. The two officers were honored for their integrity and dedication after discovering a purse containing nearly \$5,500 in cash in the Dolphin Garage and ensuring its safe return to the rightful owner. Their actions exemplify the commitment to honesty and service that defines MIA.




## MIA's Year In Review Press Conference Concourse J 3<sup>rd</sup> Floor, International Greeters Lobby



On February 24, 2025, Mayor Daniella Levine Cava hosted a televised “Year in Review” press conference at MIA during which time she provided residents and the traveling public an update on the numerous repairs, renovations and capital projects that have been completed or are underway at the airport, which will transform MIA into a modern-day, innovative state-of-the art facility over the next 10-15 years. The Mayor emphasized the progress being made with the restoration and modernization of MIA’s moving conveyances (i.e., escalators, elevators and moving sidewalks), public-access restrooms and passenger boarding bridges. Remarks were also delivered by Jimmy Morales, Miami-Dade County Chief Operating Officer; Miami-Dade Commissioners Kevin M. Cabrera and Danielle Cohen Higgins; MIA Director and CEO, Ralph Cutié; and Juan Carlos Liscano, Vice-President, American Airlines. Miami-Dade Commissioners Raquel A. Regalado and Oliver G. Gilbert, III were also in attendance as well as the “WE ARE MIA” team that works every day to enhance passenger loyalty and elevate customer satisfaction.



## **Xovis-Aero Solution Management System Installed at MIA Security Checkpoint 3**

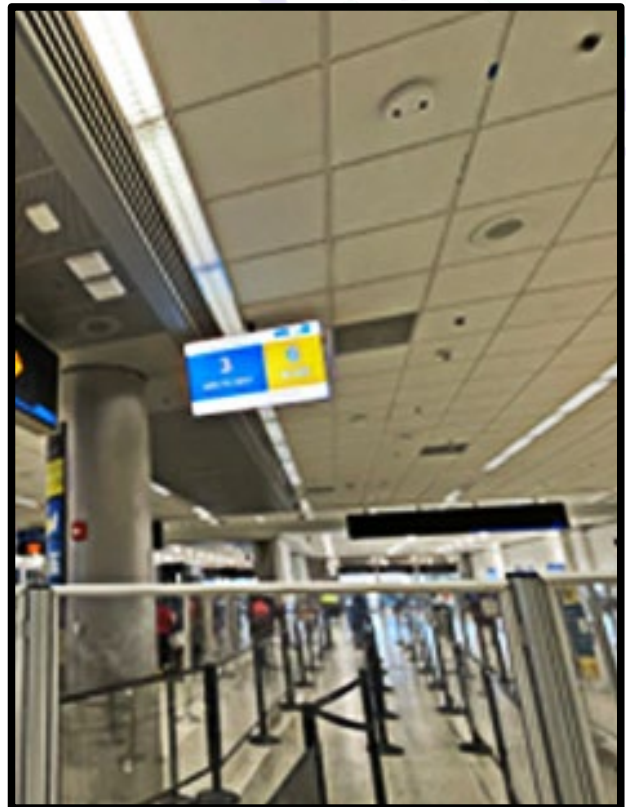


This project installed 3D sensors at Security Checkpoint 3. These sensors utilize advanced algorithms for queue management, real-time tracking and predictive modeling. The data collected from these sensors is stored enabling MIA officials to make well informed and real-time decisions regarding the effective management of checkpoint flows.





## Miami International Airport (MIA) Removal of Payphone Housing

**Before**

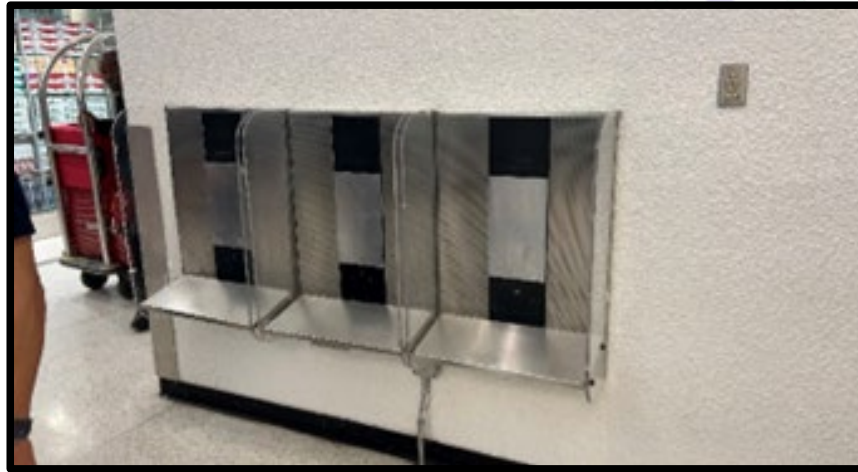

**After**




This project entailed the removal of a payphone on the wall next to an ATM machine in front of Ticket Counter 159 on the second floor by Door No. 9. The scope of work included wall repair and repainting. The task was completed February 4, 2025.



## Miami International Airport (MIA) Hallway by Security Check Point 4 Lighting Replacement

**Before**

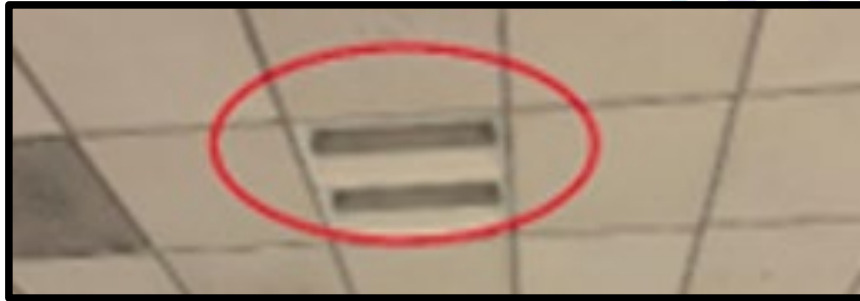

**After**



This project entailed replacing the lights in and around Security Check Point 4 hallway. This upgrade improves vision and contributes to a safer environment as the entire area is now brightly illuminated. The task was completed on January 17, 2025.



## Miami International Airport (MIA) Carpet Replacement Behind Terminal Ticket Counter 336

**Before**



**After**



This project entailed replacing the carpet behind the Spirit Airlines Ticket Counter. The upgrade improves the esthetics of the area and contributes to a safer environment. The task was completed on January 28, 2025.



## Miami International Airport (MIA) Door 12 Tile Bench and Wall Repair

**Before**

a



**After**



This project entailed the cutting, squaring and patching of a stationary tiled bench outside Door No. 12. Additional work entailed ensuring the bench was flushed and sprayed to blend in with the existing wall. The repair improves vision and contributes to a safer environment. The task was completed on January 27, 2025.





P.O. Box 123 552624  
Miami, FL 33142-5564  
[www.iflyMIA.com](http://www.iflyMIA.com)

MDC024



Miami-Dade Aviation Department: Aviation Capital Program Report  
Summary of Changes  
April 2025

**Exhibit A – Procurement Status – No Changes**

Ordinance No. 19-122	Contract Number & Description	Summary of Changes
		.

**Exhibit B – Financial Status**

Ordinance No. 19-122	Contract Number & Description	Summary of Changes
Yes	Contract No. A19-MDAD-01  MIA Terminal Wide Re-roofing and Lightning System Upgrades Miami Executive Airport	Prior Expenditures: \$6,914,208.16  Current Month Expenditures: \$0.00  Cumulative Expenditures to Date: \$6,914,208.16
Yes	Contract No. A19-MDAD-02  Notice to Professional Consultants – Facility Design Services	Prior Expenditures: \$9,696,898.36  Current Month Expenditures: \$0.00  Cumulative Expenditures to Date: \$9,696,898.36
Yes	Contract No. MDAD-CIP-V009A  Miami Executive Airport (TMB) Runway Incursion Mitigation (RIM)	Prior Expenditures: \$11,613,147.11  Current Month Expenditures: \$0.00  Cumulative Expenditures to Date: \$11,613,147.11

Miami-Dade Aviation Department: Aviation Capital Program Report  
Summary of Changes  
April 2025

Yes	Contract No. E20-MDAD-03  Photogrammetric Mapping, Topographic, Planimetric and Light Detection and Ranging (LiDar) Services	Prior Expenditures: \$2,504,942.03  Current Month Expenditures: \$3,982.94  Cumulative Expenditures to Date: \$2,508,942.97
-----	--	---



# EXHIBIT B

April 2025



FUTURE  READY



# Aviation Capital Program Report - Procurement Status

ID: 10

Status: Final Action

Accelerate Ordinance: Yes

District(s): 01, 11

Resolution #: R-842-20

Advertisement Date / COS Begins: 5/1/2020

Contract Number: MDAD-CIP-V009A

Contract Term: 609 Calendar Days to Award Recommendation Date / COS Ends: 7/30/2020

Substantial Completion

90 Calendar Days to

Final Completion

Contract Type: Invitation to Bid

Estimated Contract Amount: \$15,856,216.48

Awarded Contract Amount: \$13,301,531.44

OMB Project #: 2000001049

OMB Project Description: Rehabilitate runway 9-27 and construct run-up pad at Miami- Opa-Locka Airport;

upgrade security at Miami - Homestead General Aviation Airport; construct runway

incursion mitigation option 2- Phase 1, expand south apron for a new taxi lane,

construct a new 130-foot high Air traffic Control Tower and construct runway incursion

mitigation hot spot 1 with Taxiway H- west extension to Threshold 9R at Miami

Executive Airport.

BCC Meeting Date: September 1, 2020

BCC Committee Meeting: N/A

Firm(s) Awarded: H&R Paving, Inc.

Location(s): MIAMI EXECUTIVE AIRPORT

Project Name / Description: Miami Executive Airport (TMB) Runway Incursion Mitigation (RLIM).

Proposed Method of Award	Contract Measures	Pre-Proposal Conference / Site Visit	Proposal Due Date	Selection Committee Appt. Date:	Evaluation Meeting Date:	Oral Presentation	1st Tier / Step 1 Selection	2nd Tier / Step 2 Selection Oral Presentation	Negotiations Meeting Date(s):	Final Action Outcome
Lowest Price / Lowest Responsive, Bidder	DBE- 13.79%	Pre Proposal Conference- 5/11/2020	6/5/2020	N/A	N/A	N/A	N/A	N/A	N/A	Contract Awarded

Comments:

**Summary of Minimum Experience & Qualifications:** General Contractor: 1) The State of Florida Construction Industry Licensing Board, pursuant to the provisions of Section 489.115 of the Florida Statutes; or 2) The Miami-Dade County Construction Trades Qualifying Board, pursuant to the provisions of Section 10-3 (a) of the Miami-Dade County Code. Holders of Miami-Dade County Certificates of Competency must also hold Certificates of Registration issued by the State of Florida Construction Industry Licensing Board, pursuant to the provisions of Section 489.177, Florida Statutes.



# Aviation Capital Program Report - Procurement Status

ID: 11

Status: Final Action

Accelerate Ordinance: Yes

District(s): Various

Resolution #: R-22-22

Advertisement Date / COS Begins: 7/10/2020

Contract Number: A19-MDAD-02

Contract Term: Five (5) years

Award Recommendation Date / COS Ends: 1/19/2022

Contract Type: Notice to Professional Consultants (A/E)

Estimated Contract Amount: \$22,055,000.00

Awarded Contract Amount: \$5,513,750.00

OMB Project #: 2000000094 and 2000000096

OMB Project Description: Renovate Concourse E to include interior, exterior and code requirement upgrades; upgrade passenger loading bridges; replace automated people mover; rehabilitate apron pavement in Concourse E's Satellite and Lower concourse; implement automated processing for inbound international passengers working in conjunction with the Department of Homeland Security utilizing the latest technology and modified Transportation Security Administration (TSA) approved processes; build new chiller plant to meet preconditioned air demands; and upgrade life safety features.

Rehabilitate taxiway T and S; realign taxiway R; construct Airport Operations Control Room (AOC); construct new employee parking garage; replace Concourse E through H ticket counters; and repair MIA parking garage structure.

BCC Meeting Date: 01/19/2022

BCC Committee Meeting: N/A

Firm(s) Awarded: Carty Architecture, LLC Leo A. Daly Company Stantec Consulting Services, Inc. EXP US Services, Inc.

Location(s): ALL AIRPORTS

Project Name / Description: Facility Design Services

Proposed Method of Award	Contract Measures	Pre-Proposal Conference / Site Visit	Proposal Due Date	Selection Committee Appt. Date:	Evaluation Meeting Date:	Oral Presentation	1st Tier / Step 1 Selection	2nd Tier / Step 2 Selection Oral Presentation	Negotiations Meeting Date(s)	Final Action Outcome
Highest Ranked Firm	DBE- 28.00%	Pre-Proposal: 7/17/2020	9/23/2020	Original CSC memo was 09-25-20. The substitution CSC memo was approved on 02-08-21.	N/A	N/A	03/10/2021	N/A	05/25/2021, 5/28/2021 and 06/02/21	Contracts Awarded

Comments:

**Summary of Minimum Experience & Qualifications:** It is preferred that the Prime consultant have a cumulative five (5) years of experience within the last twenty (20) years modifying and/or designing airport facilities at major airport hubs.



# Aviation Capital Program Report - Procurement Status

ID: 12

Status: Final Action

Accelerate Ordinance: Yes

District(s): 06

Resolution #: R-807-21

Advertisement Date / COS Begins: 5/28/2020

Contract Number: A19-MDAD-01

Contract Term: 2555 Calendar Days/Seven (7) years

Award Recommendation Date / COS Ends: 9/1/2021

Contract Type: Notice to Professional Consultants (A/E)

Estimated Contract Amount: \$14,232,603.00

Awarded Contract Amount: \$14,232,603.00

OMB Project #: 2000001043

OMB Project Description: Replace roofing system for entire terminal-wide roof structure; upgrade terminal lighting protection systems; relocate tenants as required; replace passenger boarding bridges and associated equipment at north and central terminals.

BCC Meeting Date: 09/01/2021

BCC Committee Meeting: 07/13/2021

Firm(s) Awarded: EXP U.S. Services, Inc.

Location(s): MIA

Project Name / Description: MIA Terminal Wide Re-roofing and Lightning System Upgrades

Proposed Method of Award	Contract Measures	Pre-Proposal Conference / Site Visit	Proposal Due Date	Selection Committee Appt. Date:	Evaluation Meeting Date:	Oral Presentation	1st Tier / Step 1 Selection	2nd Tier / Step 2 Selection	Oral Presentation	Negotiations Meeting Date(s)	Final Action Outcome
Highest Ranked Firm	SBE- A&E 30.00% SBE- Services 2.00%	Pre-Proposal: 6/8/2020	9/2/2020	4/29/2020	10/28/2020	N/A	10/28/2020	N/A	10/28/2020	2/11/2021 and 2/18/2021	Contract Awarded

Comments: Awarded on Sept. 1, 2021 by the BCC via R-807-21.

Summary of Minimum Experience & Qualifications: It is highly preferable for the Prime to have at least one staff member that has one of the following roof Registered Water Proofing

Consultant certifications by the Roof Consultants Institute: 1. Registered Roof Consultant (RRC) certification 2. Registered Waterproofing Consultant (RWC)- individual certification 3.

Registered Exterior Wall Consultant (REWC)- individual certification 4. Registered Building Envelope Consultant (RBEC)- acquired by having the above three certifications





# Aviation Capital Program Report - Procurement Status

ID: 15

Status: Final Action

Accelerate Ordinance: Yes

District(s): Various

Resolution #: R-610-22

Advertisement Date / COS Begins: 4/23/2021

Contract Number: E20-MDAD-03

Contract Term: 5 years, plus one one-year option to renew

Award Recommendation Date / COS Ends: 7/7/2022

Contract Type: Notice to Professional Consultants (A/E)

Estimated Contract Amount: \$8,298,193.75

Awarded Contract Amount: \$8,298,193.75

OMB Project #: N/A

OMB Project Description: N/A

BCC Meeting Date: 7/7/2022

BCC Committee Meeting: 6/7/2022

Firm(s) Awarded: GPI Geospatial, Inc.

Location(s): ALL AIRPORTS

Project Name / Description: Photogrammetric Mapping, Topographic, Planimetric and Light Detection and Ranging (LiDAR) Services

Proposed Method of Award	Contract Measures	Pre-Proposal Conference / Site Visit	Proposal Due Date	Selection Committee Appt. Date:	Evaluation Meeting Date:	Oral Presentation	1st Tier / Step 1 Selection 2nd Tier / Step 2 Selection	Oral Presentation	Negotiations Meeting Date(s):	Final Action Outcome
Highest Ranked Firm	SBE A&E- 2% SBE G&S- 1%	Pre-Proposal: 04/30/2021	5/24/2021	5/12/2021	N/A	N/A	First Tier Part 1: 8/25/2021 First Tier Part 2: 10/12/2021	N/A	1/04/2022	Contract Awarded

Comments:

Summary of Minimum Experience & Qualifications: N/A



# Aviation Capital Program Report - Procurement Status

ID: 17

Status: Final Action

Accelerate Ordinance: Yes

District(s): 01, 11

Resolution #: R-205-24

Advertisement Date / COS Begins:

Contract Number: MDAD-CIP-V009A

Contract Term: 414 day extension

Award Recommendation Date / COS Ends:

Contract Type: Invitation to Bid

Estimated Contract Amount: \$0.00

Awarded Contract Amount: \$0.00

OMB Project #: 2000001049

OMB Project Description: Rehabilitate runway 9-27 and construct run-up pad at Miami- Opa-Locka Airport; upgrade security at Miami - Homestead General Aviation Airport; construct runway incursion mitigation option 2- Phase 1, expand south apron for a new taxi lane, construct a new 130-foot high Air traffic Control Tower and construct runway incursion mitigation hot spot 1 with Taxiway H- west extension to Threshold 9R at Miami Executive Airport.

BCC Meeting Date: 3/19/2024

BCC Committee Meeting: 2/22/2024

Firm(s) Awarded: H&R Paving, Inc.

Location(s): MIAMI EXECUTIVE AIRPORT • MIAMI-OPA LOCKA EXECUTIVE AIRP

Project Name / Description: Change Order No. 001

Proposed Method of Award	Contract Measures	Pre-Proposal Conference / Site Visit	Proposal Due Date	Selection Committee Appt. Date:	Evaluation Meeting Date:	Oral Presentation	1st Tier / Step 1 Selection	2nd Tier / Step 2 Selection	Negotiations Meeting Date(s):	Final Action Outcome
Lowest Price / Lowest Responsive, Responsible Bidder	DBE- 13.79%	N/A		N/A	N/A	N/A	N/A	N/A	N/A	Ratification was approved.

**Comments:** RESOLUTION RATIFYING, PURSUANT TO ORDINANCE NO. 19-122 CODIFIED AS SECTION 2-285.2 OF THE MIAMI-DADE COUNTY CODE, THE ACCEPTANCE AND EXECUTION OF CHANGE ORDER NO. 001 TO CONSTRUCTION CONTRACT NO. MDAD-CIP-V009A BETWEEN MIAMI-DADE COUNTY AND H&R PAVING INC., AUTHORIZING THE TRANSFER OF UNUSED FUNDS IN THE AMOUNT OF \$353,138.00 FROM THE CONTRACT'S PERMIT ALLOWANCE ACCOUNT TO THE GENERAL ALLOWANCE ACCOUNT AND PROVIDING FOR A 414 DAY TIME EXTENSION; AND AUTHORIZING THE COUNTY MAYOR OR COUNTY MAYOR'S DESIGNEE TO EXERCISE ALL THE PROVISIONS OF SECTION 2-285.2 OF THE CODE INCLUDING THE AUTHORITY TO RESOLVE DISPUTES, NEGOTIATE CLAIMS AND EXECUTE CHANGE ORDERS TO SAID CONTRACT.

Summary of Minimum Experience & Qualifications:





# EXHIBIT C

April 2025



FUTURE  READY



# Aviation Capital Program Report - Financial Status

Contract No.	Project Description	Project Phase	Estimated Completion Date	FY 2025-2026 Adopted Budget Amount	Current Approved Budget Amount	Prior Expenditures	Current Month Expenditures	Cumulative Expenditures to Date	Expenditures Indicator at 30%	Expenditures Indicator at 60%	Expenditures Indicator at 90%	Comments
A19-MDAD-02	Notice to Professional Consultants Facility Design and Construction Inspection Services	Awarded	09/25/25	22,055,000.00	22,055,000.00	9,696,898.36	-	9,696,898.36	X	-	-	Project awarded on 1/19/2022.
A19-MDAD-01	MIA Terminal Wide Re-roofing and Lighting System Upgrades	Awarded	09/25/27	14,232,603.00	14,232,603.00	6,914,208.16	-	6,914,208.16	X	-	-	Project awarded on 9/1/2021.
E20-MDAD-03	Photogrammetric Mapping, Topographic, Planimetric and Light Detection and Ranging (LiDAR) Services	Awarded	10/23/27	8,298,193.75	8,298,193.75	2,504,942.03	3,982.94	2,508,924.97	X	-	-	Project awarded on 7/7/2022.
MDAD-CIP-V009A	Miami Executive Airport (TMB) Runway Incursion Mitigation (RM)	Awarded	06/08/24	15,856,216.00	13,301,531.00	11,613,147.11	-	11,613,147.11	X	X	-	Project awarded on 7/30/2020.
TOTAL				60,442,012.75	57,887,327.75	30,729,195.66	3,982.94	30,733,178.60				
